


PORTER SUBDIVISION | LOTS 1 & 2

1005 & 1009 ROLLINS AVENUE, PRINCE GEORGE'S COUNTY, MARYLAND

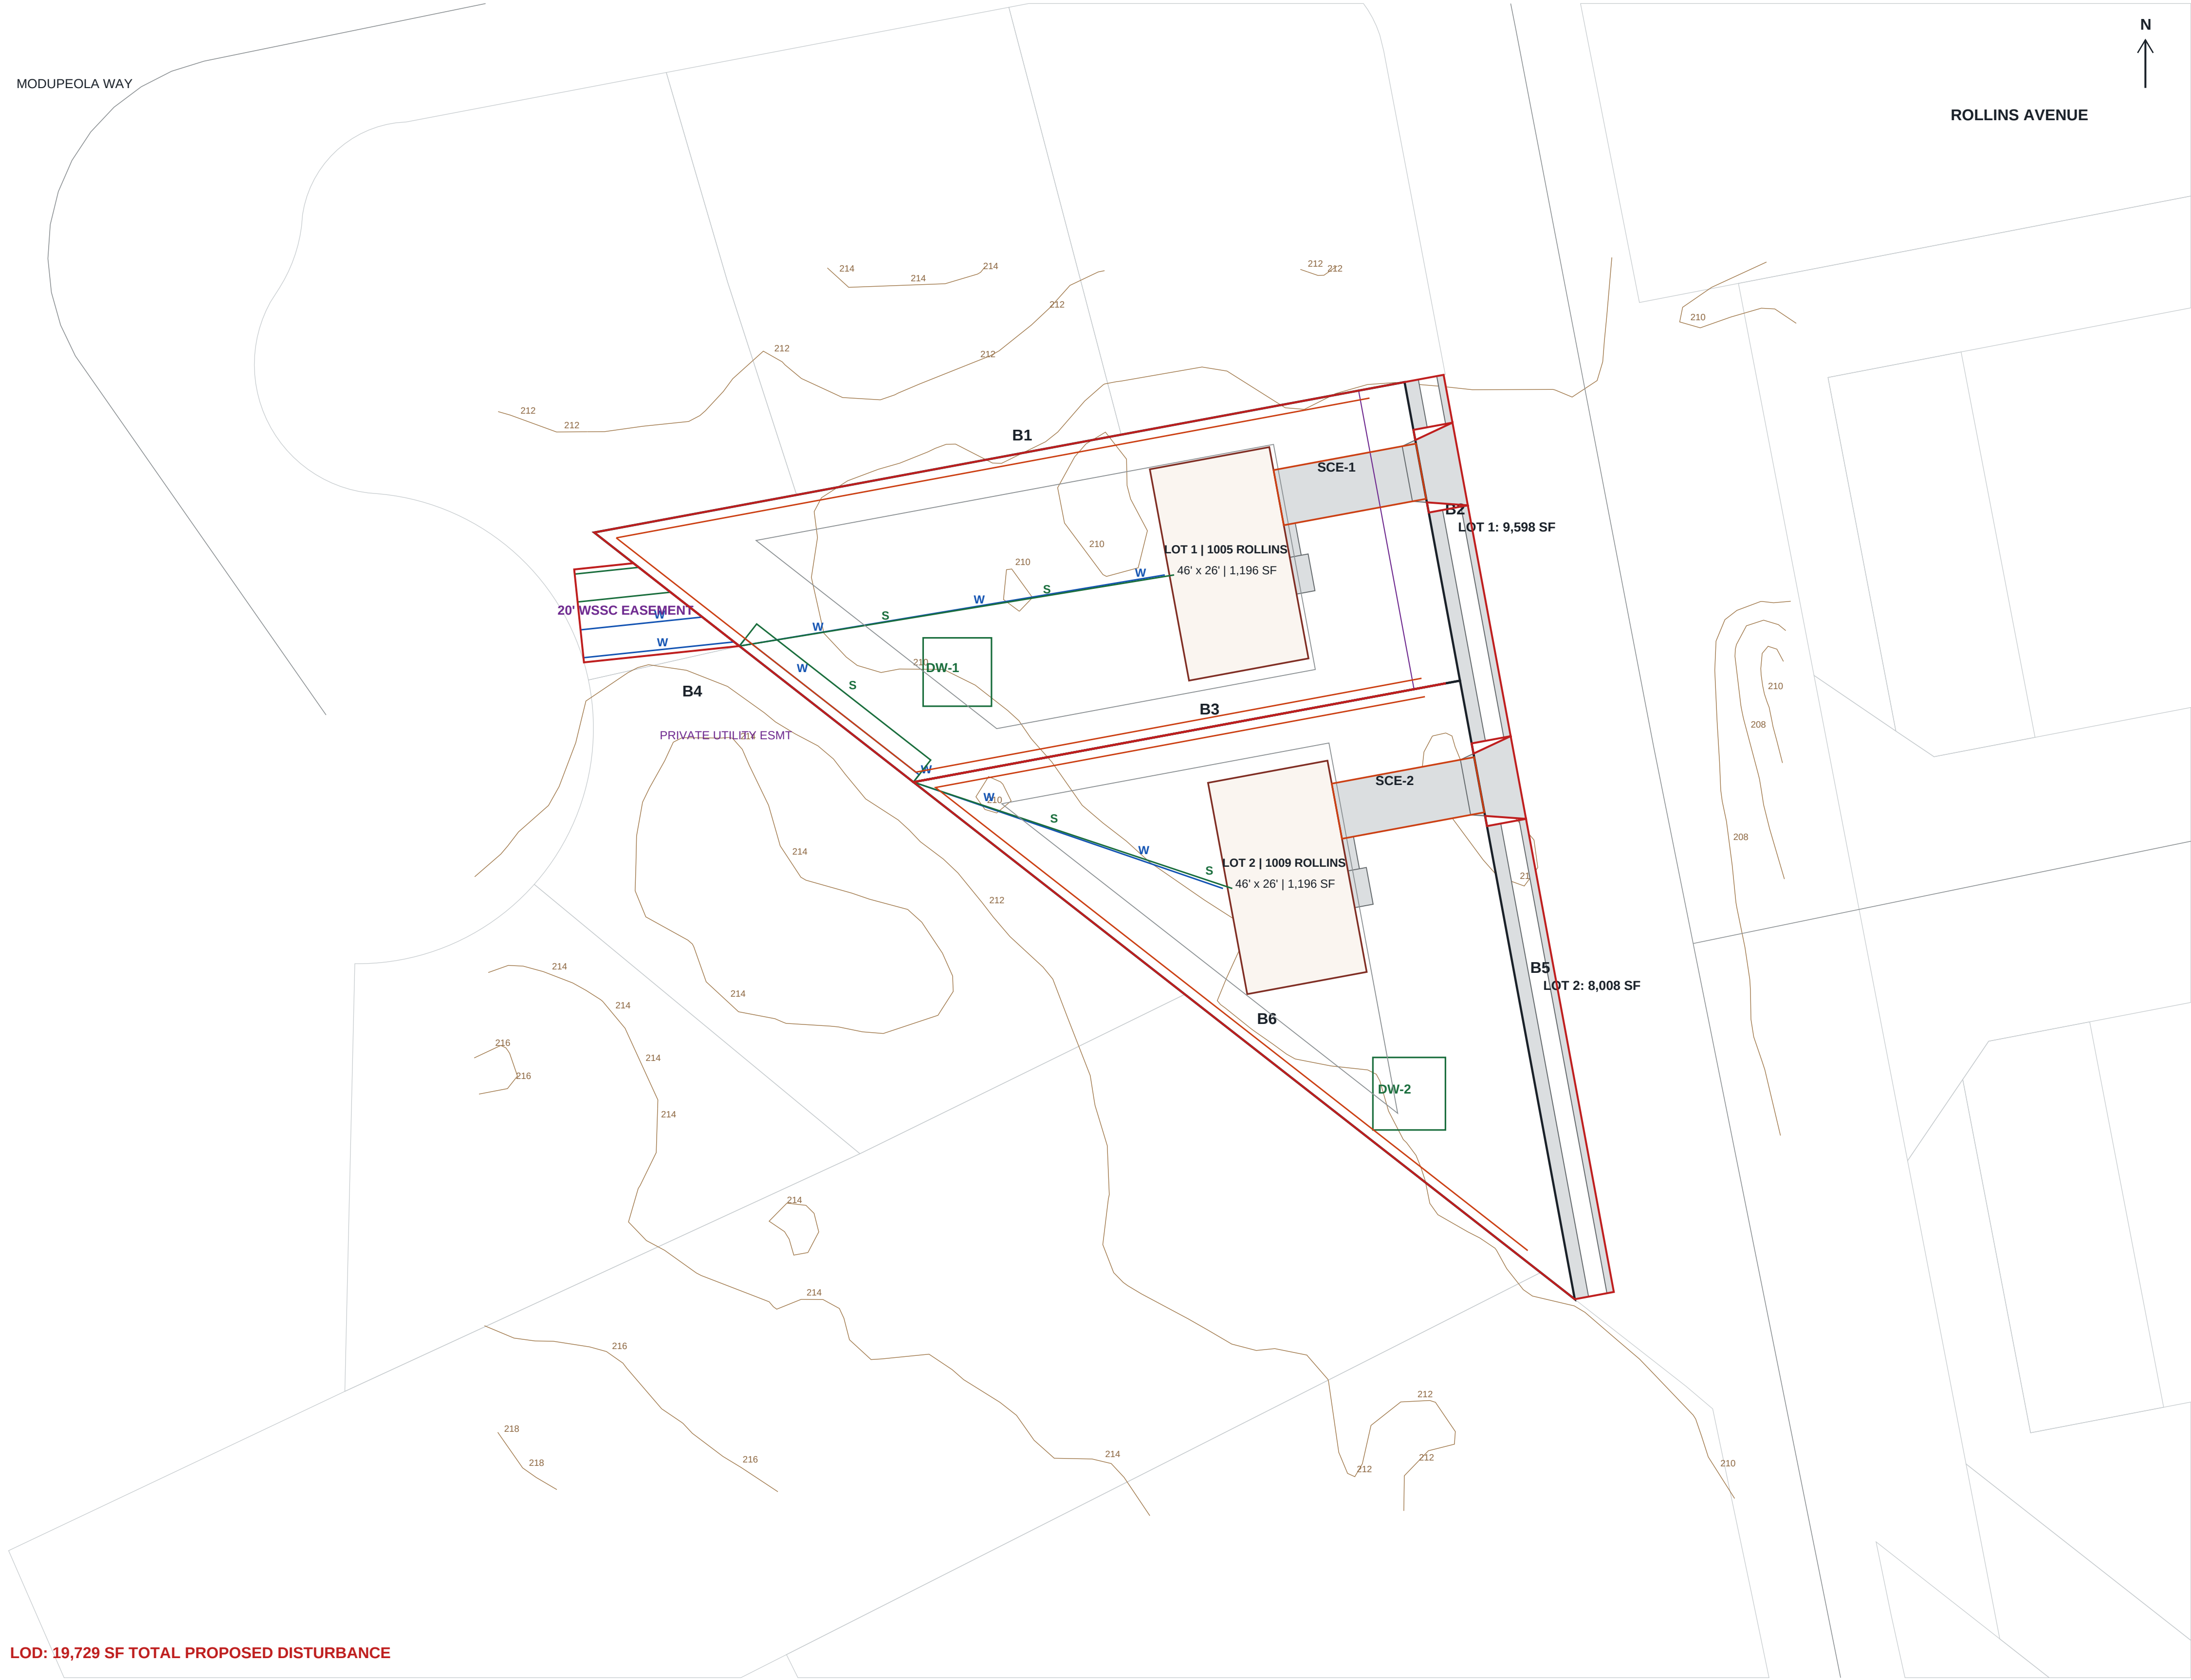

DISTURBANCE TAKEOFF

WORK AREA	POLYGON AREA
Lot 1	9,598.55 SF
Lot 2	8,008.69 SF
Frontage outside net lots	1,659.11 SF
Public utility corridor	461.99 SF
Total union (rounded up)	19,729 SF

LOD includes the full two-lot work area, shown frontage construction and the offsite utility corridor. Areas are computed from a polygon union, with no overlap double-counting. Recorded lot areas govern property data; polygon areas govern this takeoff.

CONSTRUCTION SEQUENCE

1. Obtain applicable permits and approved construction documents; hold the preconstruction meeting.
2. Locate utilities before excavation. Install perimeter controls inside the work limits and protect adjoining land.
3. Establish stabilized access at the proposed driveways (SCE-1 / SCE-2); maintain the public pedestrian route.
4. Stage Lot 1 then Lot 2; expose only the area under active construction. Keep stockpiles and washout within controlled work areas.
5. Construct foundations and utility services; protect reserved drywell locations from compaction and sediment.
6. Complete permanent drainage facilities after contributing areas are stabilized; complete frontage and final landscaping.
7. Remove temporary controls only after permanent stabilization and inspector authorization.

STANDARD STABILIZATION NOTE

Following initial soil disturbance or re-disturbance, permanent or temporary stabilization must be completed within: a.) Three (3) calendar days as to the surface of all perimeter dikes, swales, ditches, perimeter slopes, and all slopes steeper than 3 horizontal to 1 vertical (3:1); and b.) Seven (7) calendar days as to all other disturbed or graded areas on the project site not under active grading.

CONTROL DETAILS AND LIMITS

Orange dashed perimeter line: proposed sediment barrier, placed inside lot limits. Final barrier type, lengths, storage and tributary area must follow the approved sediment-control design. SCE footprints use the driveway work areas; extend stabilized access as required by the approving authority. This layout does not claim erosion-control approval.
