

KEALEE

design, build, deliver

PROJECT
1005 Rollins Ave
ADDRESS
1005 Rollins Ave
JURISDICTION
prince georges md
ZONE
RSF-65
SHEET
C-000 — Cover Sheet, Approvals and General Notes
SCALE
1" = 20'
STATUS
PRELIMINARY
SHEET NO.
1 OF 6
COORDINATES
EPSG:2248
H: NAD83
V: NAVD83 (feet)

SITE DATA		
ZONE	RSF-65	
TAX PARCEL ID	1005 Rollins Ave	
GROSS LOT AREA	9,599 SF	0.220 AC
LOT FRONTAGE	45' MIN	65.00'
SETBACKS	REQUIRED	PROVIDED
FRONT YARD	23'	23'
SIDE YARD	8'	8'
REAR YARD	20'	20'
COVERAGE	MAX	PROPOSED
LOT COVERAGE	35%	12.5%
BUILDING FOOTPRINT	—	1,196 SF
DATA		
HORIZONTAL	EPSG:2248	NAD83
VERTICAL	NAVD83 (feet)	

SITE ANALYSIS	
1. Gross lot area	9,599 SF
2. Area of dwelling	1,196 SF
3. Wooded area	NOT ESTABLISHED
4. Floodplain area	NOT ESTABLISHED
5. Net lot area	9,599 SF
6. TOTAL AREA DISTURBED	NOT QUANTIFIED

SEQUENCE OF CONSTRUCTION	
1. Pre-construction meeting	1 DAY
2. Obtain necessary permits	2 DAYS
3. Notify MVA Utility at 811 at least 48 hours prior to any excavation	1 DAY
4. Construct stabilized construction entrance and perimeter sediment control	2 DAYS
5. Rough grade, construct dwelling, utilities and driveway	12 MONTHS
6. Fine grade and stake out all disturbed areas	1 DAY
7. Remove sediment control devices when written permission has been granted	1 DAY
TOTAL ESTIMATED TIME OF CONSTRUCTION: 12 MONTHS	

GENERAL NOTES

- CONTRACTOR SHALL CONTACT MISS UTILITY AT 811 A MINIMUM OF 48 HOURS PRIOR TO ANY EXCAVATION. FIELD VERIFY LOCATION AND DEPTH BY TEST PIT BEFORE CONSTRUCTION.
- ALL EXISTING AND PROPOSED UTILITIES SHOWN PER PGC CODE SEC. 32.106.
- PROPOSED GRADE SHOWN SOLID EXISTING GRADE SHOWN DASHED.
- ROUGH EARTHWORK GRADES AND UTILITY ELEVATIONS SHOWN TO TENTHS OF A FOOT.
- BOUNDARY SHOWN IS THE RECORDED PLAT OF SUBDIVISION — PORTER SUBDIVISION, PLAT BOOK PM 231 P.50 — TRANSCRIBED AND CHECKED FOR CLOSURE. THE PLAT IS THE BOUNDARY SURVEY. NO FIELD TOPOGRAPHY IS INCLUDED. EXISTING GRADE IS COUNTY LIDAR CONTOUR MAPPING.
- CONNECT TO EXISTING PAVEMENT, CURB AND GUTTER, DRIVEWAY AND SIDEWALK IN LINE AND GRADE.

PLAT OF RECORD

Porter Subdivision, Plat Book PM 231 p.50

NOTES OF RECORD

- BASED ON: GEOMETRIC Maryland State Plane Coordinate System (NAD 83).
- BOUNDARY OF RECORD transcribed from the recorded plat; traverse closes 1.84327', 9599 SF computed against 9,599 SF recorded.
- A transcription is not a field survey. Monumentation is not verified here.

The surveyor certifies, under declaration and approval signatures of the recorded plat are NOT reproduced here; they shall be the responsibility of the client.

LEGEND

- PROPERTY BOUNDARY
- BRL — BUILDING RESTRICTION LINE
- PROPOSED STRUCTURE
- EXISTING CONTOUR — PGATLAS 2 FT (2023), NAVD83
- STREET CENTRELINE
- PROPOSED PAVEMENT — DRIVEWAY / WALK
- EASEMENT

PRINCE GEORGE'S COUNTY SOL CONSERVATION DISTRICT APPROVAL

SEDIMENT CONTROL, CRACKING, SOLS & DRAINAGE



SIGNATURE DATE

DPE SITEROAD PLAN REVIEW DIVISION APPROVAL

SIGNATURE DATE

REVISIONS

— NONE —

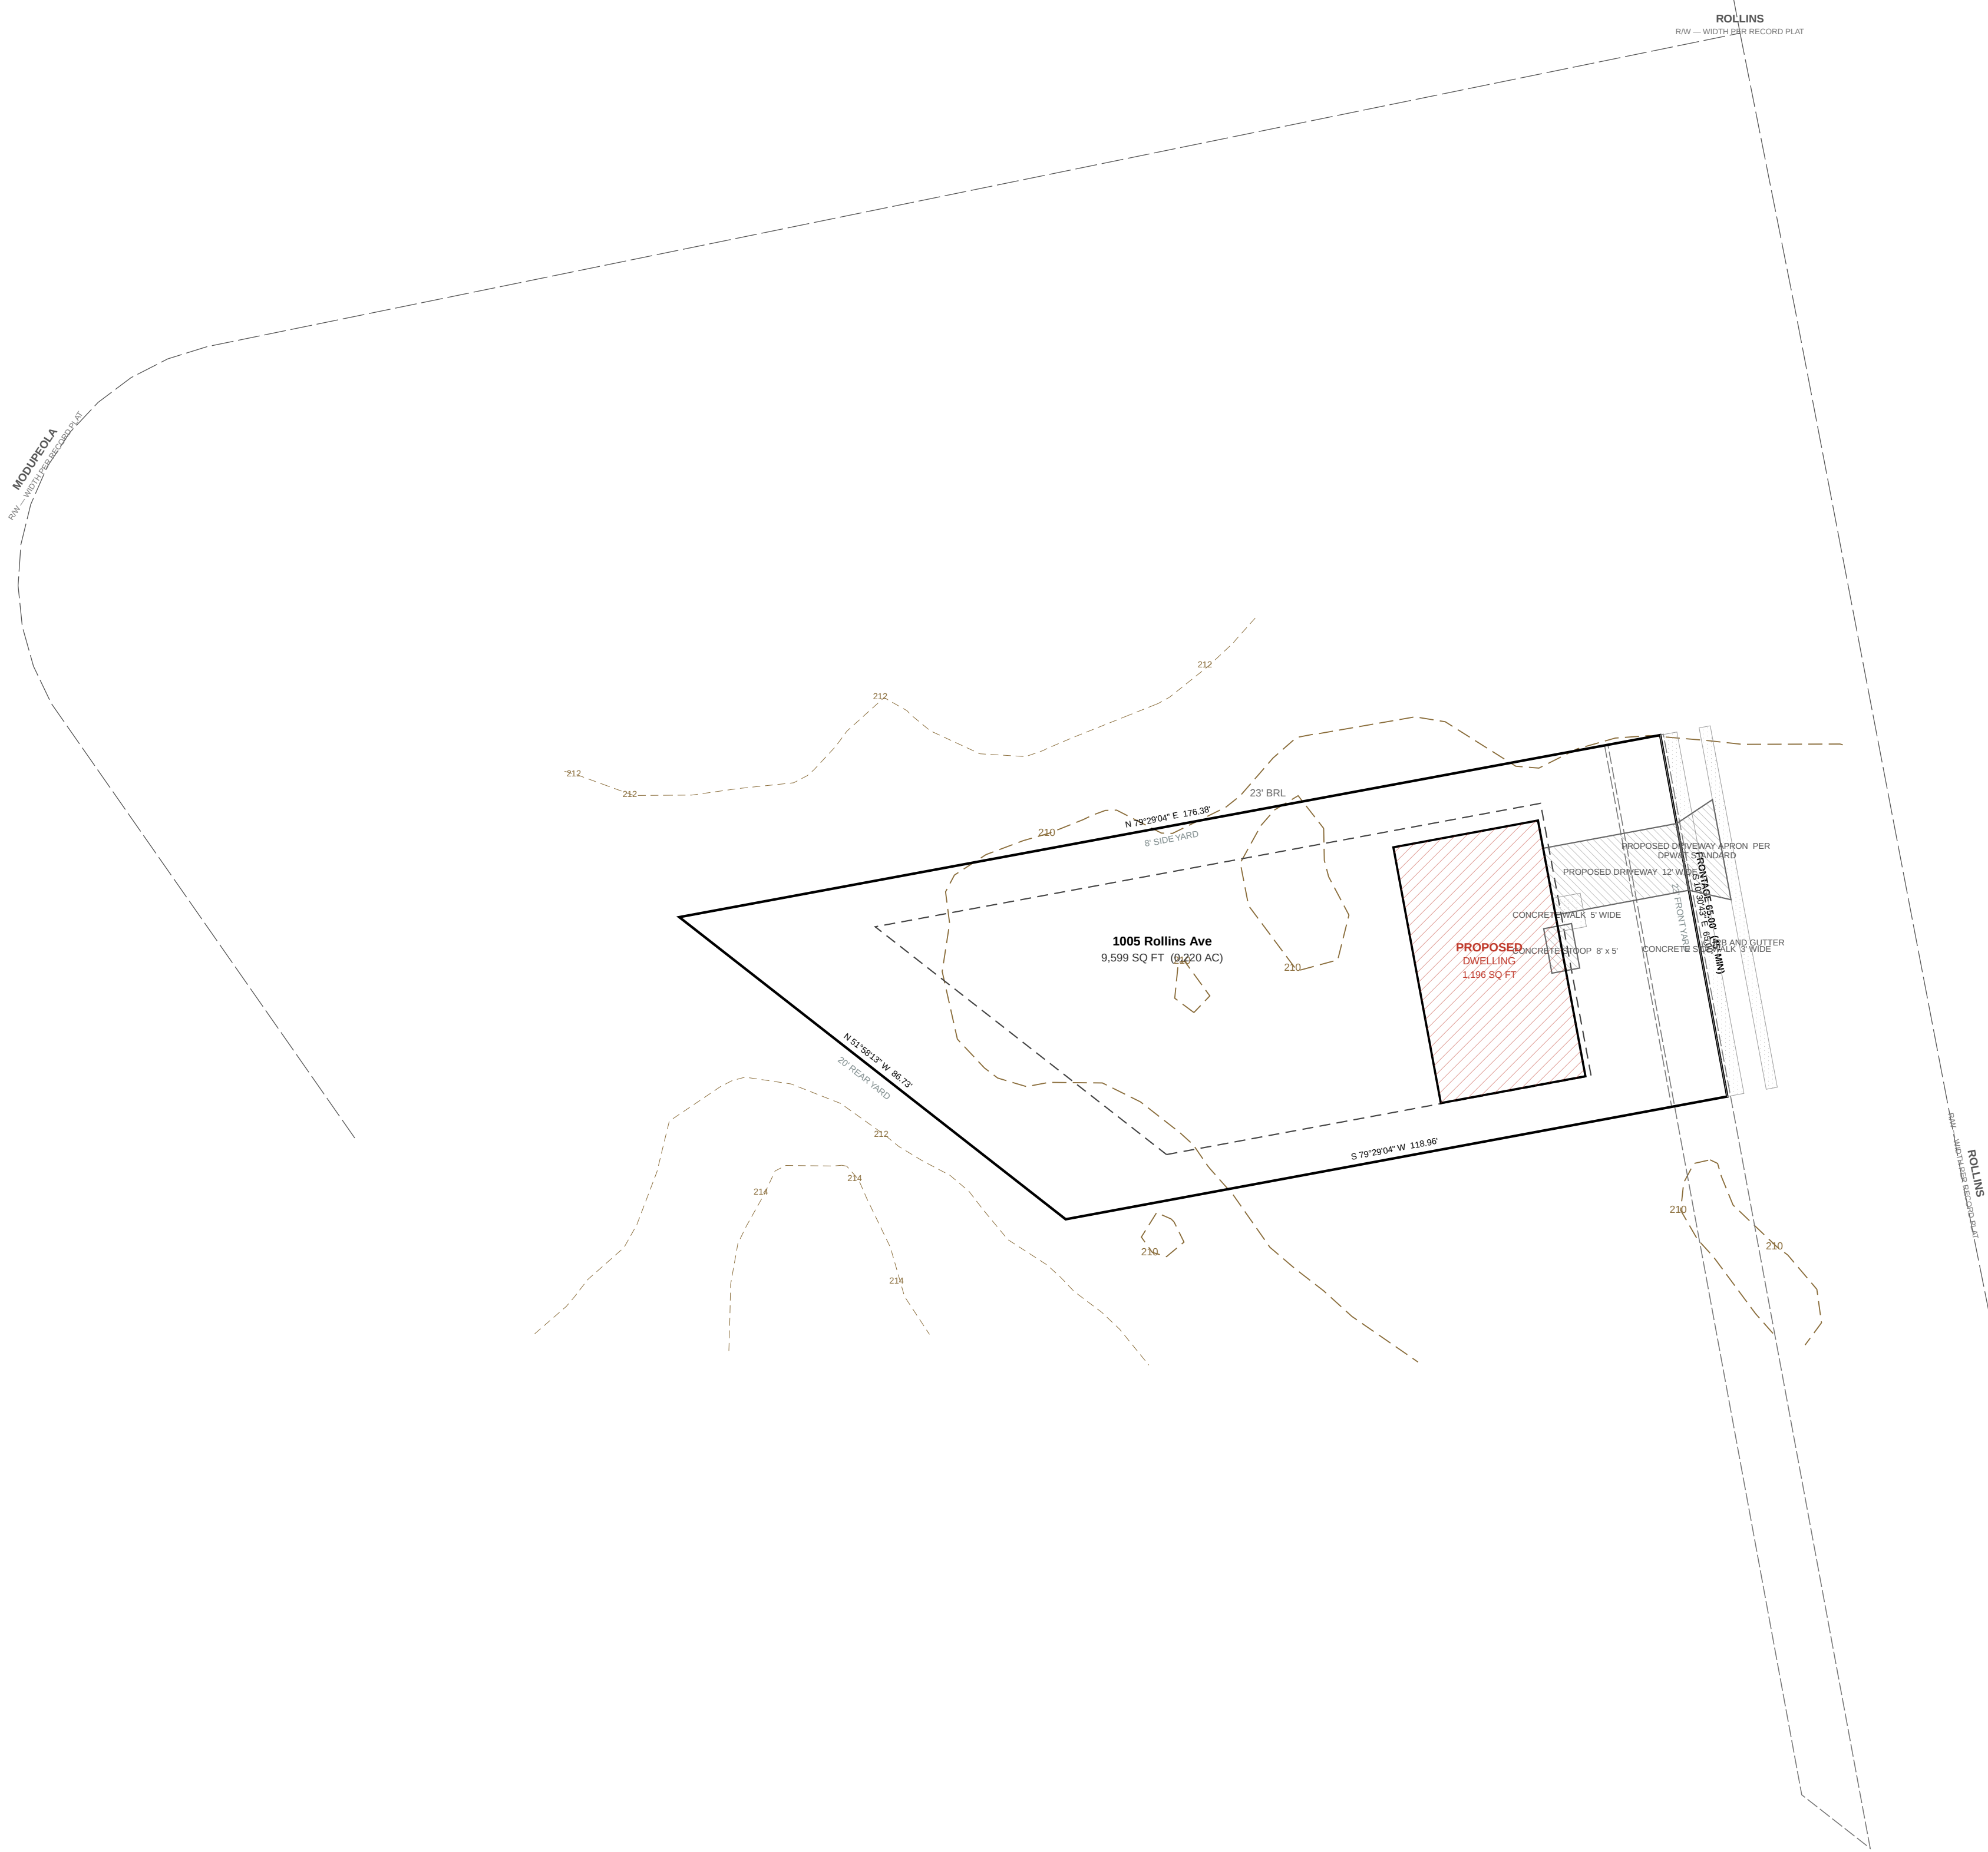

KEALEE

design, build, deliver

PROJECT
1005 Rollins Ave
ADDRESS
1005 Rollins Ave
JURISDICTION
prince georges md
ZONE
RSF-65
SHEET
C-100 — Existing Conditions and Boundary Plan
SCALE
1" = 20'
STATUS
PRELIMINARY
SHEET NO.
2 OF 6
COORDINATES
EPSG:2248
H: NAD83
V: NAVD83 (feet)

SITE DATA		
ZONE	RSF-65	
TAX PARCEL ID	1005 Rollins Ave	
GROSS LOT AREA	9,599 SF	0.220 AC
LOT FRONTAGE	45' MIN	65.00'
SETBACKS	REQUIRED	PROVIDED
FRONT YARD	23'	23'
SIDE YARD	8'	8'
REAR YARD	20'	20'
COVERAGE	MAX	PROPOSED
LOT COVERAGE	35%	12.5%
BUILDING FOOTPRINT	—	1,196 SF
DATA		
HORIZONTAL	EPSG:2248	NAD83
VERTICAL	NAVD83 (feet)	

SITE ANALYSIS	
1. Gross tract area	9,599 SF
2. Area of dwelling	1,196 SF
3. Wooded area	NOT ESTABLISHED
4. Floodplain area	NOT ESTABLISHED
5. Net tract area	9,599 SF
6. TOTAL AREA DISTURBED	NOT QUANTIFIED

SEQUENCE OF CONSTRUCTION	
1. Pre-construction meeting	1 DAY
2. Obtain necessary permits	2 DAYS
3. Notify M&D Utility at 811 at least 48 hours prior to any excavation	1 DAY
4. Construct stabilized construction entrance and perimeter sediment control	2 DAYS
5. Rough grade, construct dwelling, utilities and driveway	12 MONTHS
6. Fine grade and stabilize all disturbed areas	1 DAY
7. Remove sediment control devices when written permission has been granted	1 DAY
TOTAL ESTIMATED TIME OF CONSTRUCTION: 12 MONTHS	

GENERAL NOTES

- CONTRACTOR SHALL CONTACT MISS UTILITY AT 811 A MINIMUM OF 48 HOURS PRIOR TO ANY EXCAVATION. FIELD VERIFY LOCATION AND DEPTH BY TEST PIT BEFORE CONSTRUCTION.
- ALL EXISTING AND PROPOSED UTILITIES SHOWN PER PGC CODE SEC. 32.106.
- PROPOSED GRADE SHOWN SOLID EXISTING GRADE SHOWN DASHED.
- ROUGH EARTHWORK GRADES AND UTILITY ELEVATIONS SHOWN TO TENTHS OF A FOOT.
- BOUNDARY SHOWN IS THE RECORDED PLAT OF SUBDIVISION — PORTER SUBDIVISION, PLAT BOOK PM 231 P.50 — TRANSCRIBED AND CHECKED FOR CLOSURE. THE PLAT IS THE BOUNDARY SURVEY. NO FIELD TOPOGRAPHY IS INCLUDED. EXISTING GRADE IS COUNTY LIDAR CONTOUR MAPPING.
- CONNECT TO EXISTING PAVEMENT, CURB AND GUTTER, DRIVEWAY AND SIDEWALK IN LINE AND GRADE.

PLAT OF RECORD

Porter Subdivision, Plat Book PM 231 p.50

NOTES OF RECORD

- BASED ON: GEOMETRIC Maryland State Plane Coordinate System (NAD 83).
- BOUNDARY OF RECORD transcribed from the recorded plat; traverse closes 1.84327, 9599 SF computed against 9,599 SF recorded.
- A transcription is not a field survey. Monumentation is not verified here.

The surveyor certifies, under declaration and approval signatures of the recorded plat are NOT reproduced here; they exist in the instrument, not in this drawing.

LEGEND	
—	PROPERTY BOUNDARY
- - - - -	BRL — BUILDING RESTRICTION LINE
—	PROPOSED STRUCTURE
—	EXISTING CONTOUR — PGATLAS 2 FT (2023), NAVD83
—	STREET CENTRELINE
—	PROPOSED PAVEMENT — DRIVEWAY / WALK
- - - - -	EASEMENT

PRINCE GEORGE'S COUNTY SOL CONSERVATION DISTRICT APPROVAL

SEDIMENT CONTROL, CRACKING, SOILS & DRAINAGE



SIGNATURE	DATE
-----------	------


DPE SITEROAD PLAN REVIEW DIVISION APPROVAL

SIGNATURE	DATE
-----------	------

REVISIONS

— NONE —

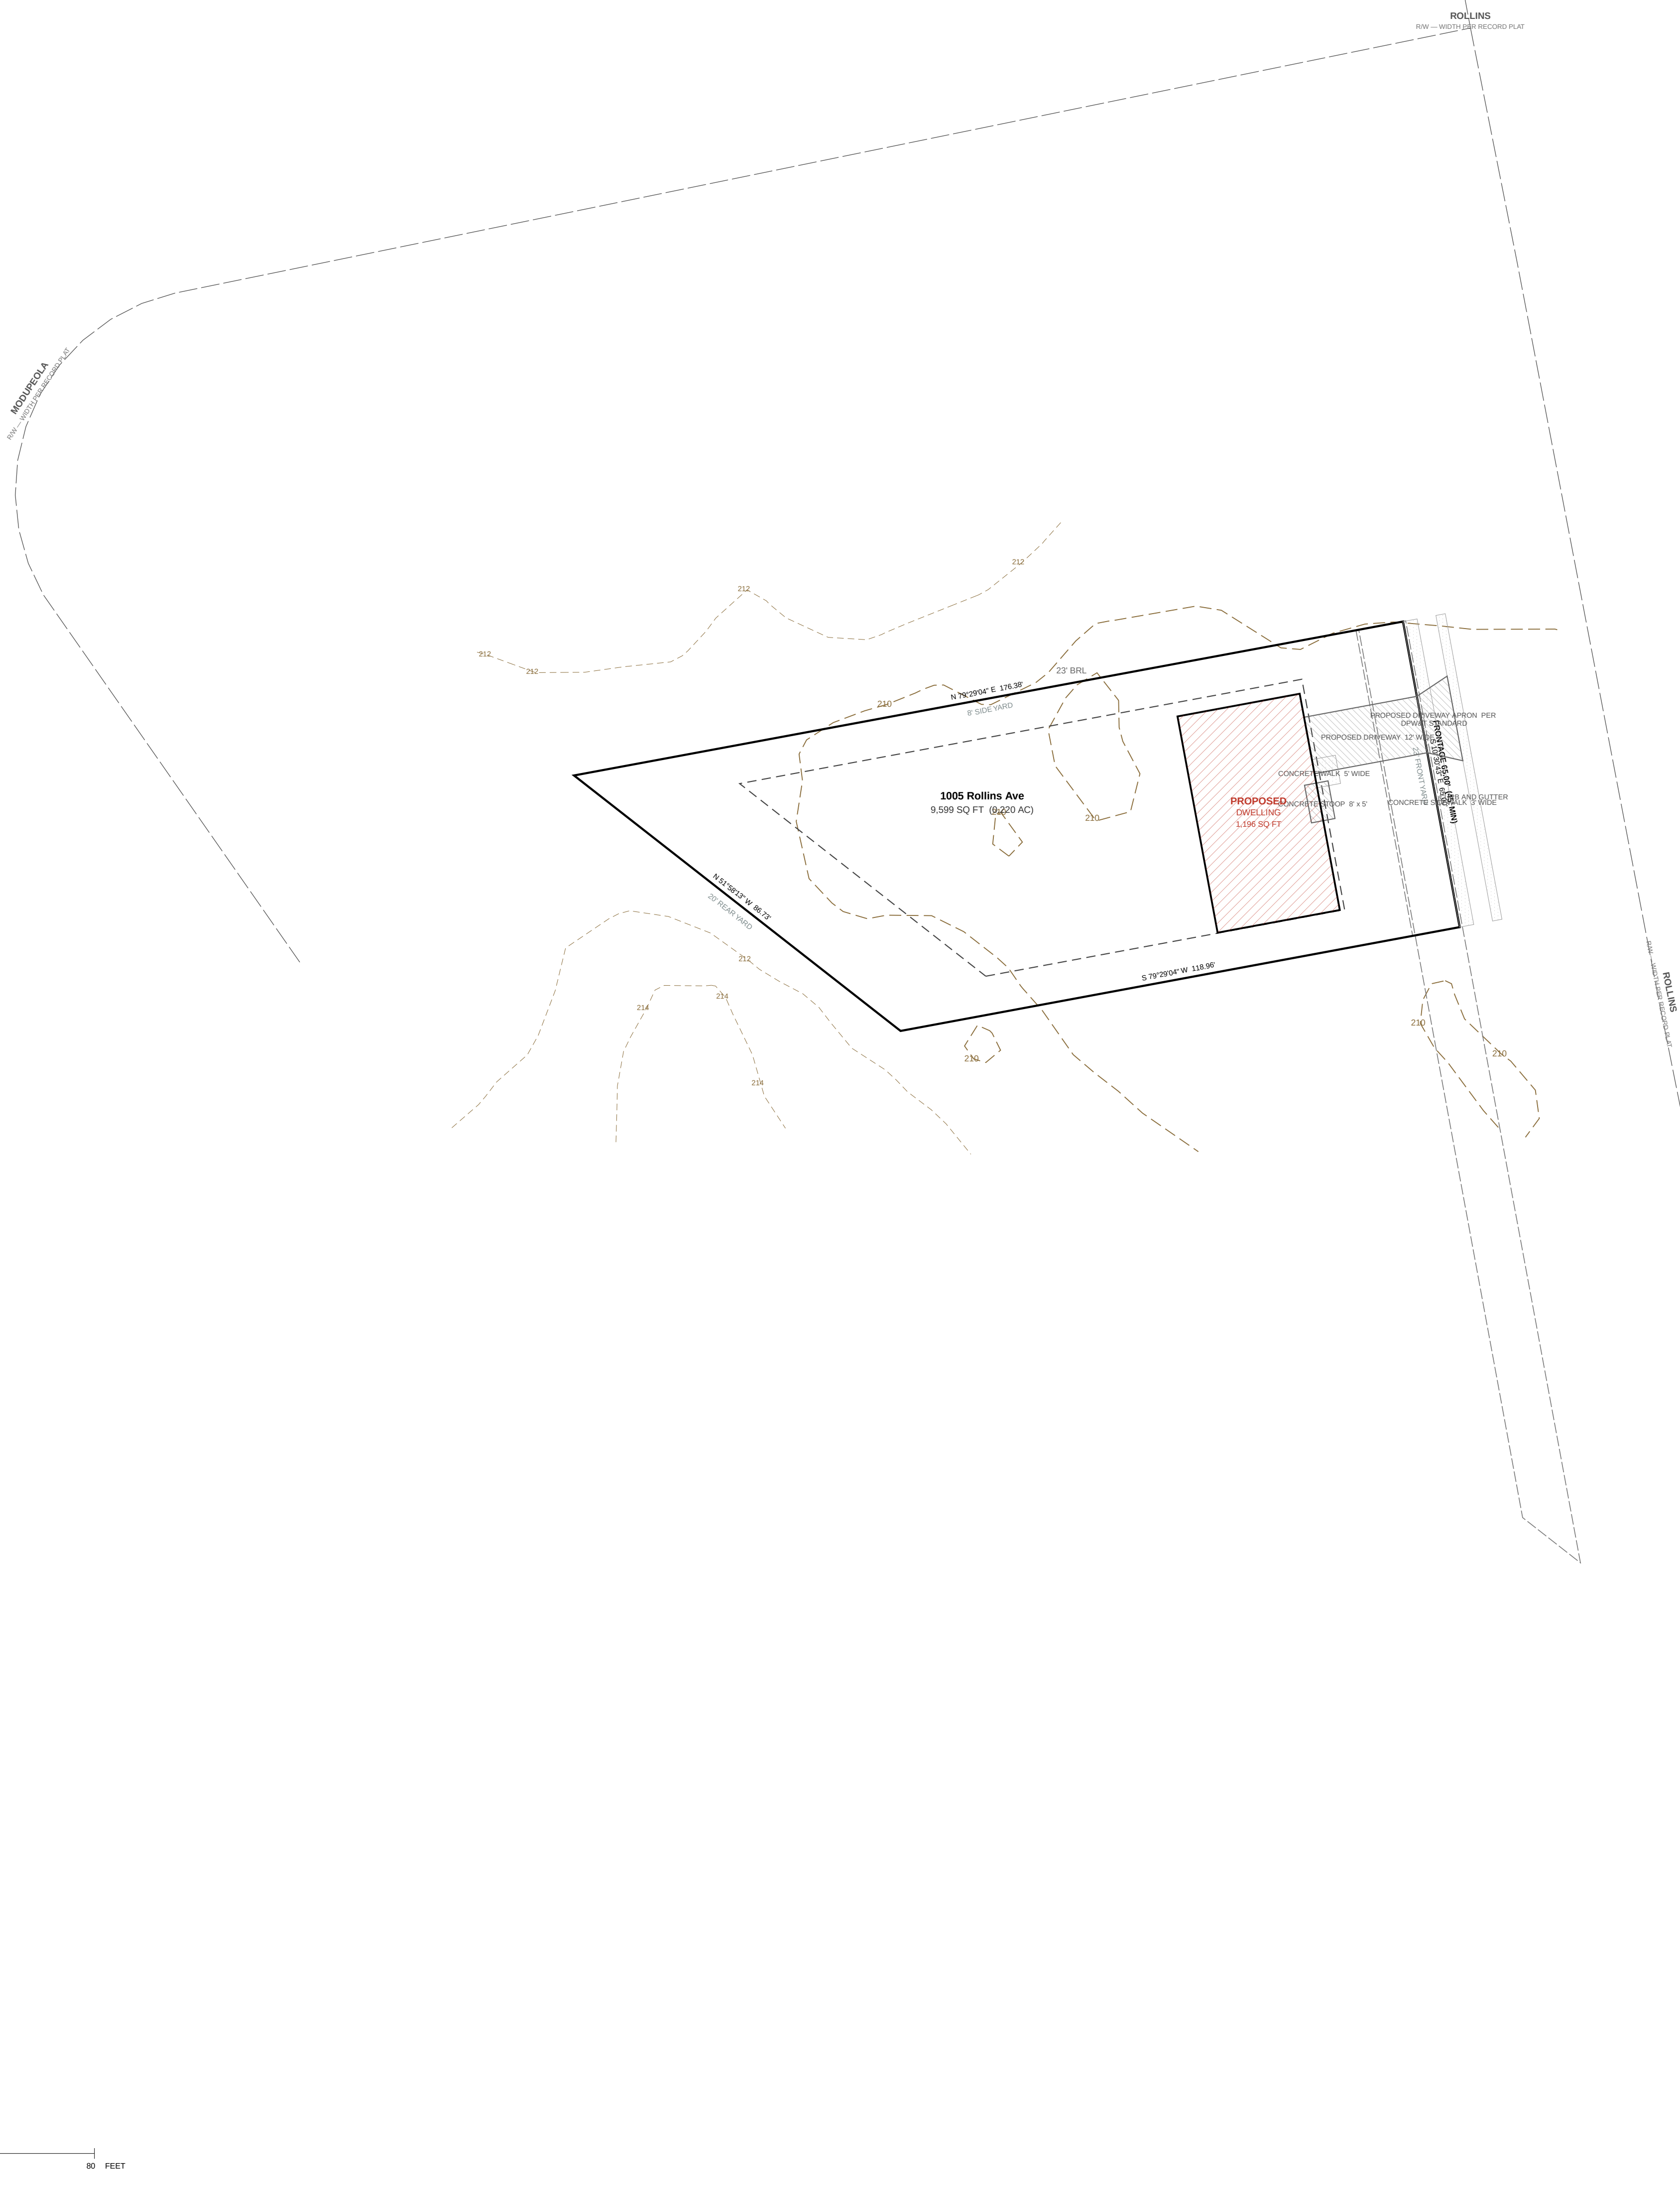

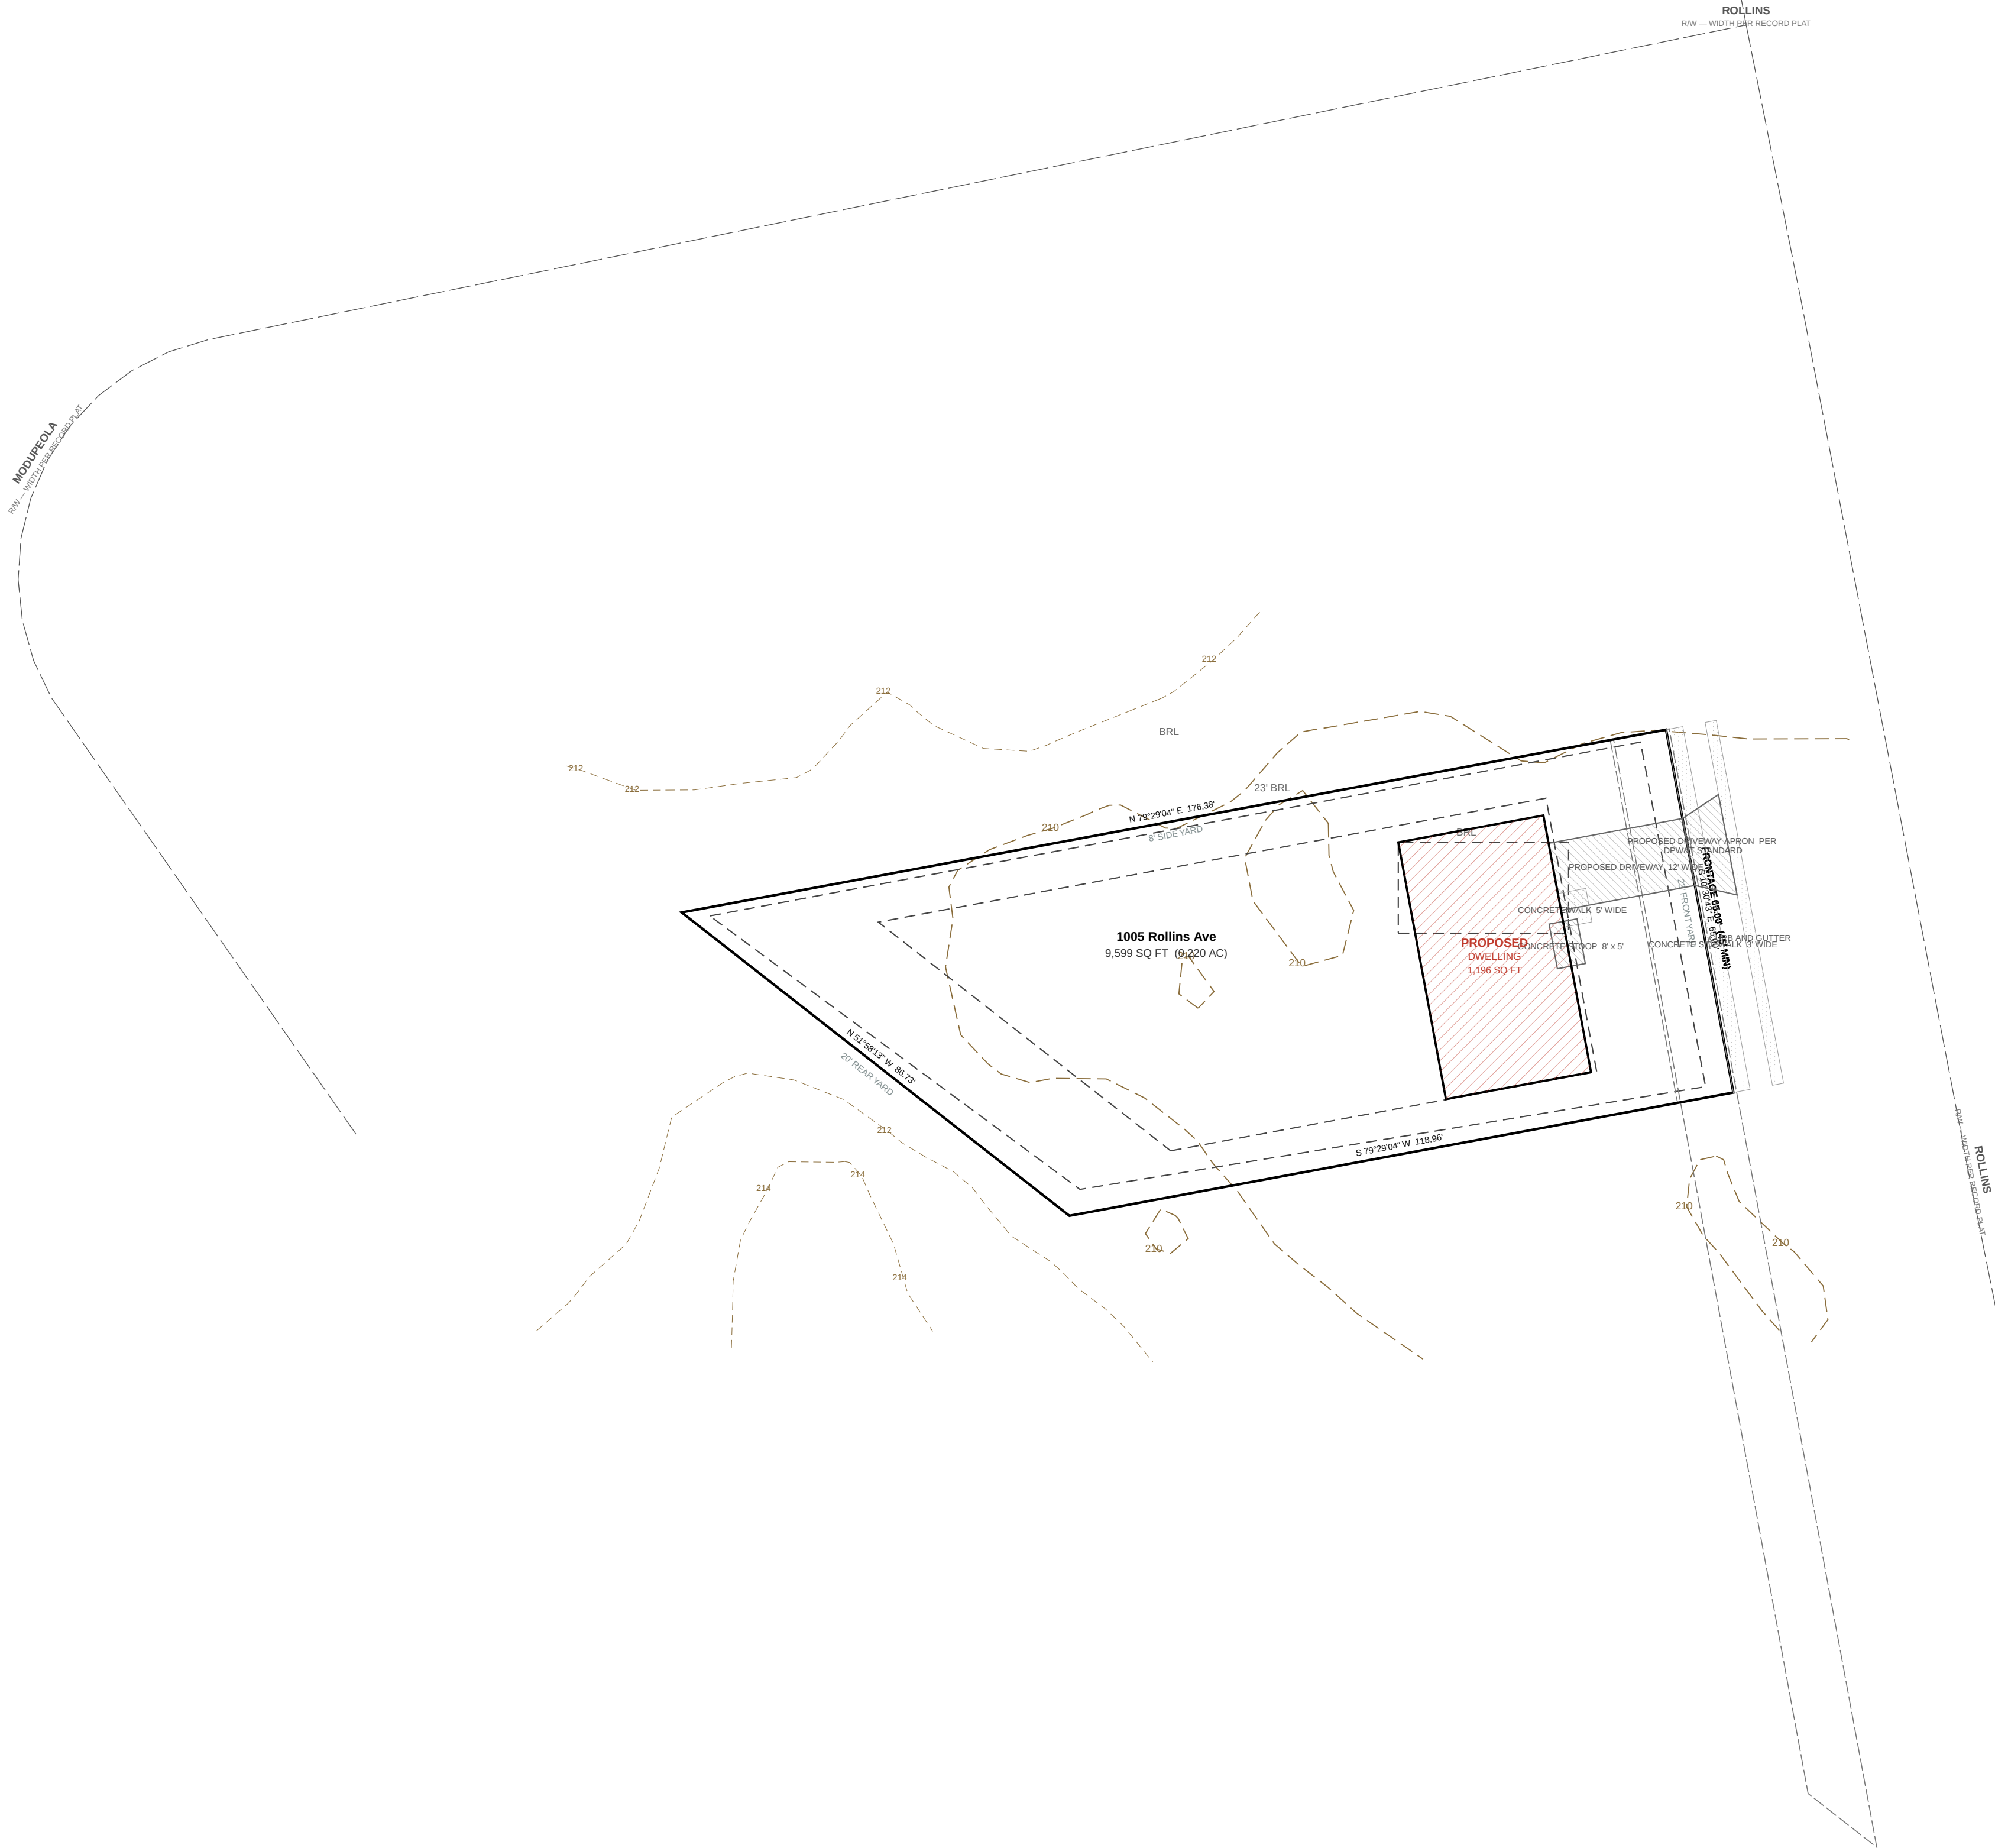

KEALEE
design, build, deliver

PROJECT
1005 Rollins Ave
ADDRESS
1005 Rollins Ave
JURISDICTION
prince georges md
ZONE
RSF-65
SHEET
C-200 — Overall Site and Zoning Plan
SCALE
1" = 20'
STATUS
PRELIMINARY
SHEET NO.
3 OF 6
COORDINATES
EPSG:2248
H: NAD83
V: NAVD83 (feet)

SITE DATA		
ZONE	RSF-65	
TAX PARCEL ID	1005 Rollins Ave	
GROSS LOT AREA	9,599 SF	0.220 AC
LOT FRONTAGE	45' MIN	65.00'
SETBACKS	REQUIRED	PROVIDED
FRONT YARD	23'	23'
SIDE YARD	8'	8'
REAR YARD	20'	20'
COVERAGE	MAX	PROPOSED
LOT COVERAGE	35%	12.5%
BUILDING FOOTPRINT	—	1,196 SF
DATA		
HORIZONTAL	EPSG:2248	NAD83
VERTICAL	NAVD83 (feet)	

SITE ANALYSIS	
1. Gross tract area	9,599 SF
2. Area of dwelling	1,196 SF
3. Wooded area	NOT ESTABLISHED
4. Floodplain area	NOT ESTABLISHED
5. Net tract area	9,599 SF
6. TOTAL AREA DISTURBED	NOT QUANTIFIED

SEQUENCE OF CONSTRUCTION	
1. Pre-construction meeting	1 DAY
2. Obtain necessary permits	2 DAYS
3. Notify M&A Utility at B11 at least 48 hours prior to any excavation	1 DAY
4. Construct stabilized construction entrance and perimeter sediment control	2 DAYS
5. Rough grade, construct dwelling, utilities and driveway	12 MONTHS
6. Fine grade and stabilize all disturbed areas	1 DAY
7. Remove sediment control devices when written permission has been granted	1 DAY
TOTAL ESTIMATED TIME OF CONSTRUCTION: 12 MONTHS	

GENERAL NOTES

- CONTRACTOR SHALL CONTACT MISS UTILITY AT B11 A MINIMUM OF 48 HOURS PRIOR TO ANY EXCAVATION. FIELD VERIFY LOCATION AND DEPTH BY TEST PIT BEFORE CONSTRUCTION.
- ALL EXISTING AND PROPOSED UTILITIES SHOWN PER PGC CODE SEC. 32.106.
- PROPOSED GRADE SHOWN SOLID EXISTING GRADE SHOWN DASHED.
- ROUGH EARTHWORK GRADES AND UTILITY ELEVATIONS SHOWN TO TENTHS OF A FOOT.
- BOUNDARY SHOWN IS THE RECORDED PLAT OF SUBDIVISION — PORTER SUBDIVISION, PLAT BOOK PM 231 P.50 — TRANSCRIBED AND CHECKED FOR CLOSURE. THE PLAT IS THE BOUNDARY SURVEY. NO FIELD TOPOGRAPHY IS INCLUDED. EXISTING GRADE IS COUNTY LIDAR CONTOUR MAPPING.
- CONNECT TO EXISTING PAVEMENT, CURB AND GUTTER, DRIVEWAY AND SIDEWALK IN LINE AND GRADE.

PLAT OF RECORD

Porter Subdivision, Plat Book PM 231 p.50

NOTES OF RECORD

- BOUNDARY OF RECORD transcribed from the recorded plat; traverse closes 1.84327, 9599 SF computed against 9,599 SF recorded.
- A transcription is not a field survey. Monumentation is not verified here.

The surveyor certifies, under declaration and approval signatures of the recorded plat are NOT reproduced here; they exist in the instrument, not in this drawing.

LEGEND

- PROPERTY BOUNDARY
- BRL — BUILDING RESTRICTION LINE
- PROPOSED STRUCTURE
- EXISTING CONTOUR — PGATLAS 2 FT (2023), NAVD83
- STREET CENTRELINE
- PROPOSED PAVEMENT — DRIVEWAY / WALK
- EASEMENT

PRINCE GEORGE'S COUNTY SOL CONSERVATION DISTRICT APPROVAL

SEDIMENT CONTROL, CRACKING, SOILS & DRAINAGE


SIGNATURE DATE

DPE STEREOAD PLAN REVIEW DIVISION APPROVAL

SIGNATURE DATE

REVISIONS

— NONE —



KEALEE

design, build, deliver

PROJECT
1005 Rollins Ave
ADDRESS
1005 Rollins Ave
JURISDICTION
prince georges md
ZONE
RSF-65
SHEET
C-400 — Grading and Drainage Plan
SCALE
1" = 20'
STATUS
PRELIMINARY
SHEET NO.
4 OF 6
COORDINATES
EPSG:2248
H: NAD83
V: NAVD83 (feet)

SITE DATA		
ZONE	RSF-65	
TAX / PARCEL ID	1005 Rollins Ave	
GROSS LOT AREA	9,599 SF	0.220 AC
LOT FRONTAGE	45' MIN	65.07'
SETBACKS	REQUIRED	PROVIDED
FRONT YARD	23'	23'
SIDE YARD	8'	8'
REAR YARD	20'	20'
COVERAGE	MAX	PROPOSED
LOT COVERAGE	35%	12.9%
BUILDING FOOTPRINT	—	1,196 SF
DATA		
HORIZONTAL	EPSG:2248	NAD83
VERTICAL	NAVD83 (feet)	

SITE ANALYSIS	
1. Gross flat area	9,599 SF
2. Area of dwelling	1,196 SF
3. Wooded area	NOT ESTABLISHED
4. Floodplain area	NOT ESTABLISHED
5. Net flat area	9,599 SF
6. TOTAL AREA DISTURBED	NOT QUANTIFIED

SEQUENCE OF CONSTRUCTION	
1. Pre-construction meeting	1 DAY
2. Obtain necessary permits	2 DAYS
3. Notify MVA Utility at 811 at least 48 hours prior to any excavation	1 DAY
4. Construct stabilized construction entrance and perimeter sediment control	2 DAYS
5. Rough grade; construct dwelling, utilities and driveway	12 MONTHS
6. Fine grade and stabilize all disturbed areas	1 DAY
7. Remove sediment control devices when written permission has been granted	1 DAY
TOTAL ESTIMATED TIME OF CONSTRUCTION: 12 MONTHS	

GENERAL NOTES

- CONTRACTOR SHALL CONTACT MISS UTILITY AT 811 A MINIMUM OF 48 HOURS PRIOR TO ANY EXCAVATION. FIELD VERIFY LOCATION AND DEPTH BY TEST PIT BEFORE CONSTRUCTION.
- ALL EXISTING AND PROPOSED UTILITIES SHOWN PER PG&E CODE SEC. 32.106.
- PROPOSED GRADE SHOWN SOLID EXISTING GRADE SHOWN DASHED.
- ROUGH EARTHWORK GRADES AND UTILITY ELEVATIONS SHOWN TO TENTHS OF A FOOT.
- BOUNDARY SHOWN IS THE RECORDED PLAT OF SUBDIVISION — PORTER SUBDIVISION, PLAT BOOK PM 231 p.50 — TRANSCRIBED AND CHECKED FOR CLOSURE. THE PLAT IS THE BOUNDARY SURVEY. NO FIELD TOPOGRAPHY IS INCLUDED. EXISTING GRADE IS COUNTY LIDAR CONTOUR MAPPING.
- CONNECT TO EXISTING PAVEMENT, CURB AND GUTTER, DRIVEWAY AND SIDEWALK IN LINE AND GRADE.

PLAT OF RECORD

Porter Subdivision, Plat Book PM 231 p.50

NOTES OF RECORD

- BASIS OF BEARING: Maryland State Plane Coordinate System (NAD 83).
- BOUNDARY OF RECORD transcribed from the recorded plat; traverse closes 1.84327', 9599 SF computed against 9,599 SF recorded.
- A transcription is not a field survey. Monumentation is not verified here.

The surveyor certifies, under declaration and approval signatures of the recorded plat and NOT reproduced here, they adhere to the requirements set forth in this document.

LEGEND	
— — — — —	PROPERTY BOUNDARY
- - - - -	BRL — BUILDING RESTRICTION LINE
— — — — —	PROPOSED STRUCTURE
— — — — —	EXISTING CONTOUR — PG&E LAS 2 FT (2023), NAVD83
— — — — —	STREET CENTRELINE
— — — — —	PROPOSED PAVEMENT — DRIVEWAY / WALK
- - - - -	EASEMENT

PRINCE GEORGE'S COUNTY SOL CONSERVATION DISTRICT APPROVAL

SEDIMENT CONTROL, CRACKING, SOILS & DRAINAGE

SIGNATURE	DATE
-----------	------

DPE STEREOAD PLAN REVIEW DIVISION APPROVAL

SIGNATURE	DATE
-----------	------

GRADING CERTIFICATE

I HEREBY CERTIFY THAT THIS PLAN CONFORMS TO THE REQUIREMENTS OF SUBTITLE 32, DIVISION 2 OF THE CODE OF PRINCE GEORGE'S COUNTY WATER RESOURCES PROTECTION AND GRADING CODE, AND THAT I OR MY STAFF HAVE INSPECTED THIS SITE, AND THAT DRAINAGE FLOWS FROM UPLAND PROPERTIES ONTO THIS SITE, AND FROM THIS SITE ONTO DOWNHILL PROPERTIES, HAVE BEEN ADDRESSED IN SUBSTANTIAL ACCORDANCE WITH APPLICABLE CODES, STANDARDS, SPECIFICATIONS, AND DATED BY A PROFESSIONAL ENGINEER LICENSED IN THE STATE OF MARYLAND.

Prince George's County DPE, Site Rough Grading Design Review Checklist, Item A.10

STABILIZATION COMPLIANCE PREAMBLE

Stabilization practices on all projects must be in compliance with the requirements of COMAR 26.17.01 by January 9, 2013, regardless of when an erosion and sediment control plan was approved.

COMAR 26.17.01 (b)(3), Greenkeeping of approved plans



STANDARD STABILIZATION NOTE


Following final soil disturbance or re-disturbance, permanent or temporary stabilization must be completed within: a) Three (3) calendar days as to the surface of all perimeter dikes, swales, ditches, perimeter slopes, and all slopes steeper than 3:1 horizontal to 1:1 vertical (3:1); and b) Seven (7) calendar days as to all other disturbed or graded areas on the project site not under active grading.

(2013 Maryland Standards and Specifications for Soil Erosion and Sediment Control, "Standard Stabilization Note" (adopted by COMAR 26.17.01.09A)(3))

REVISIONS

— NONE —

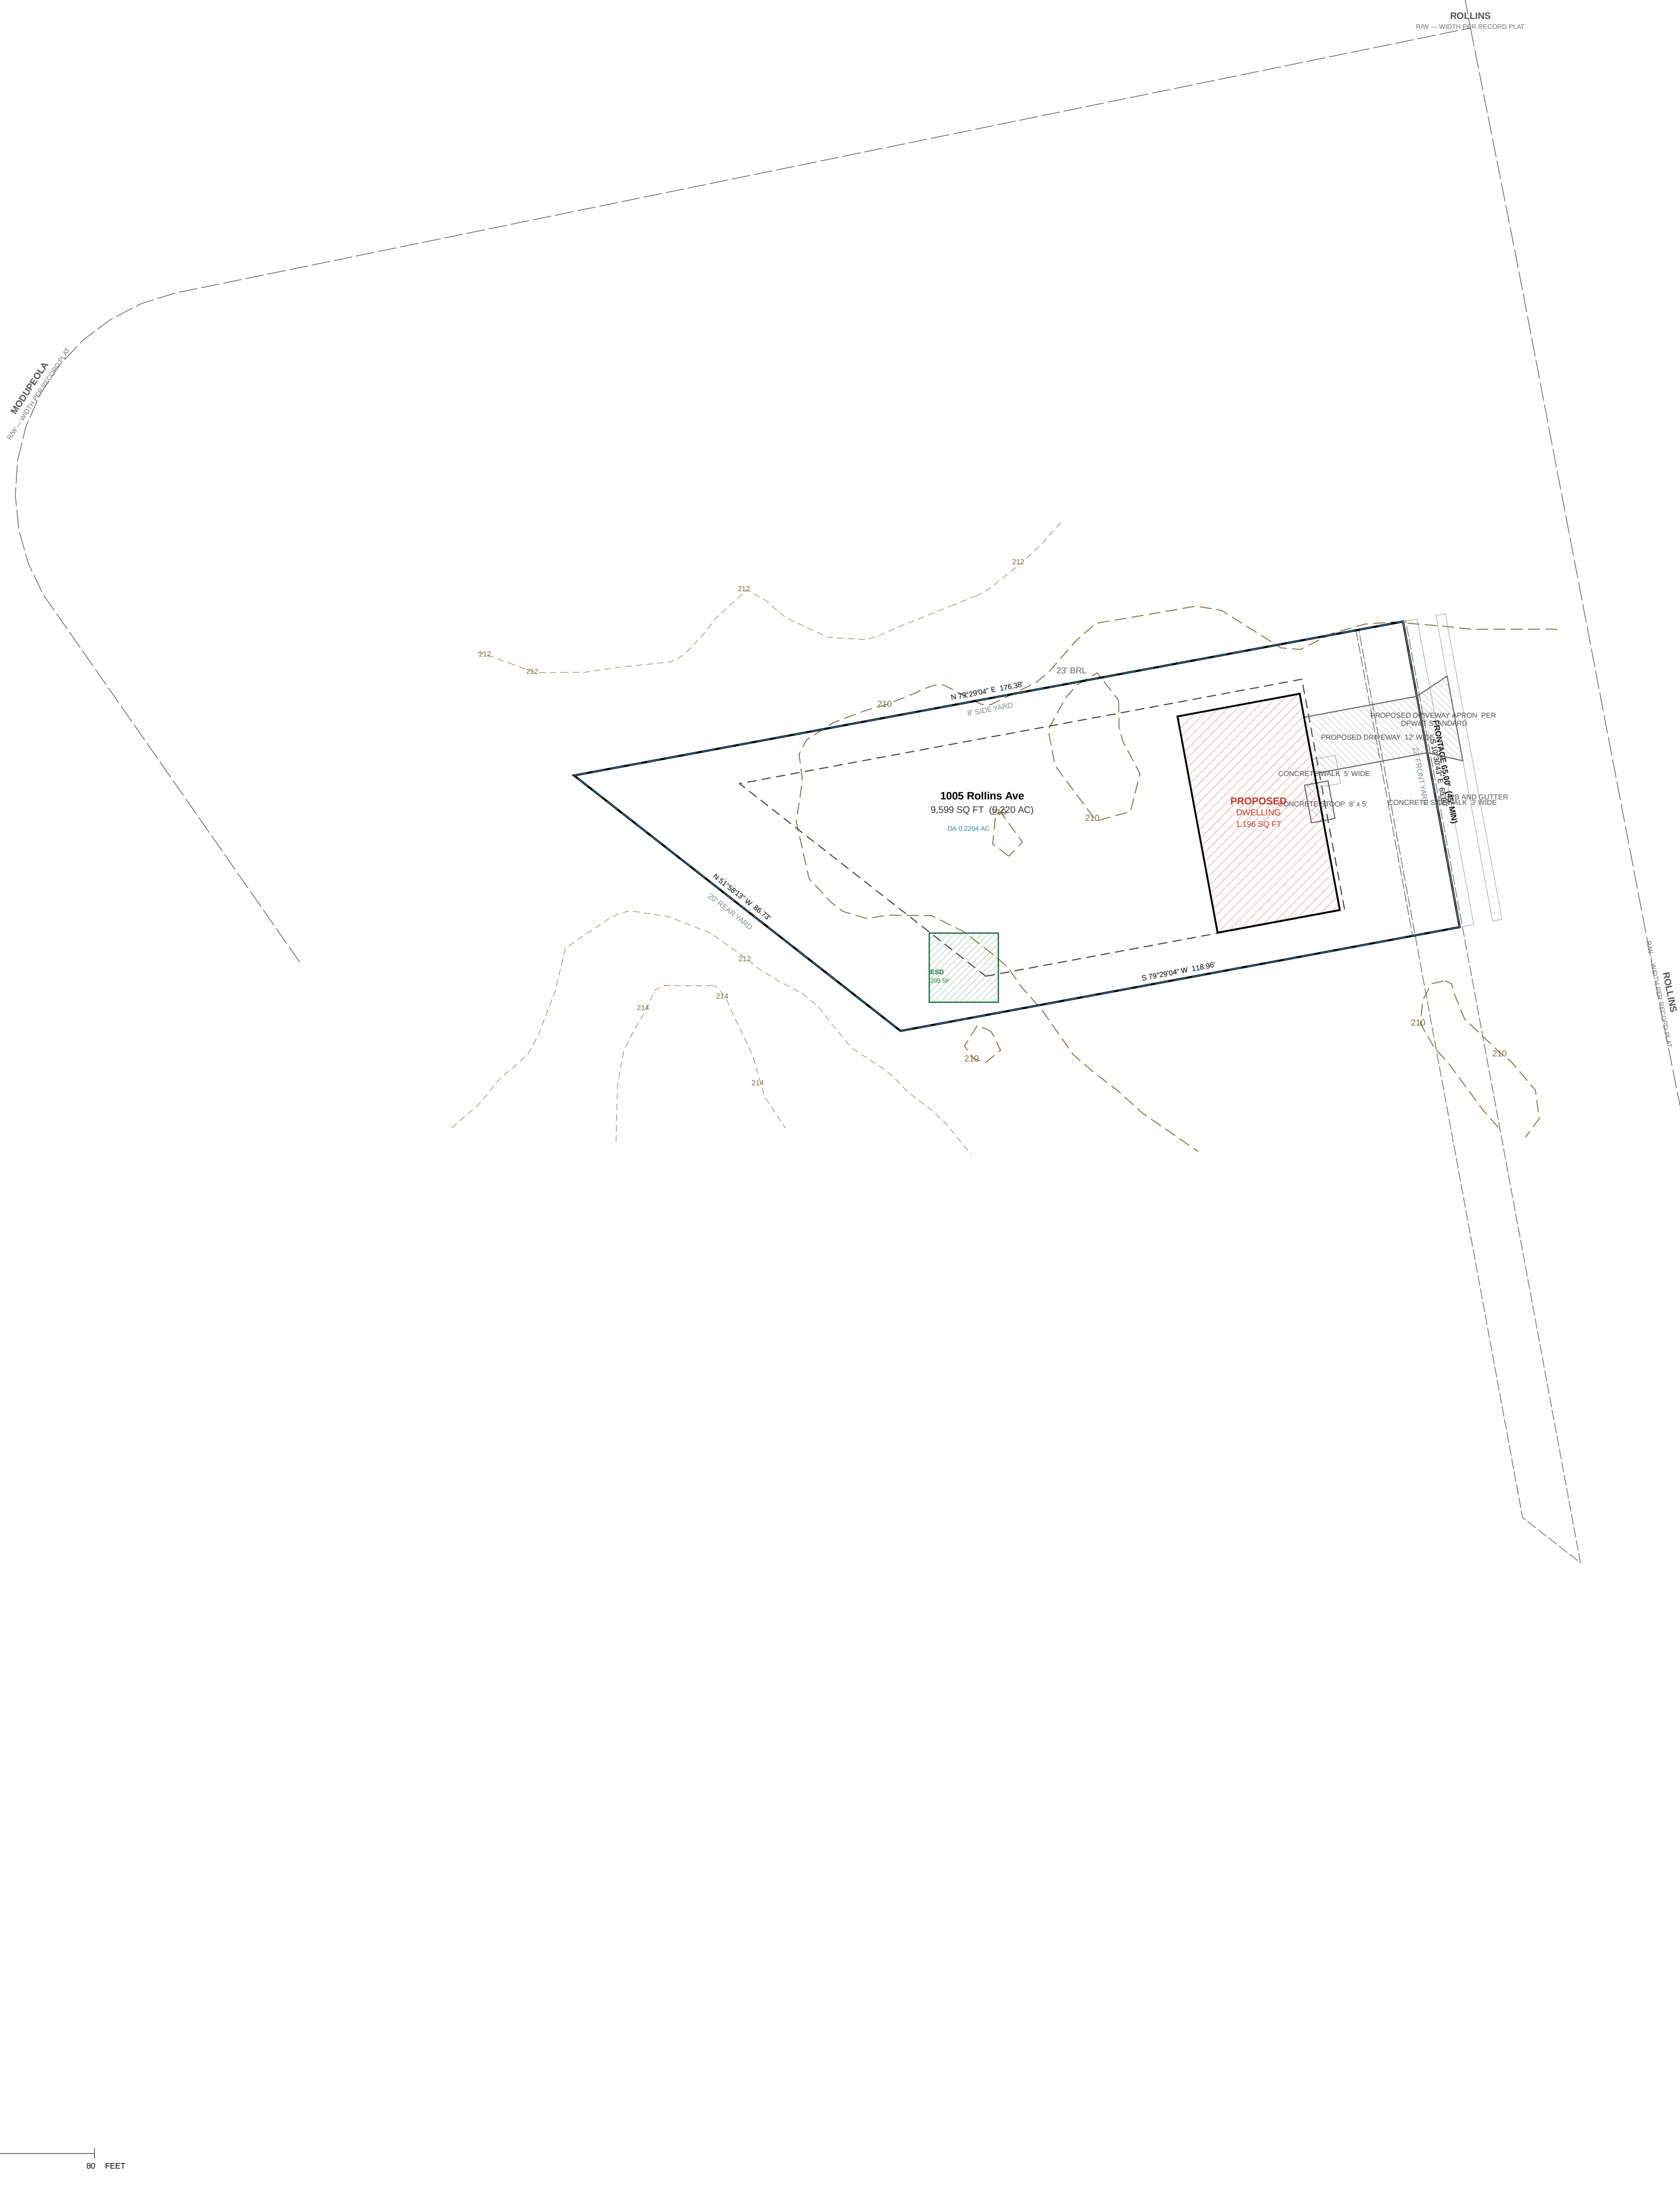

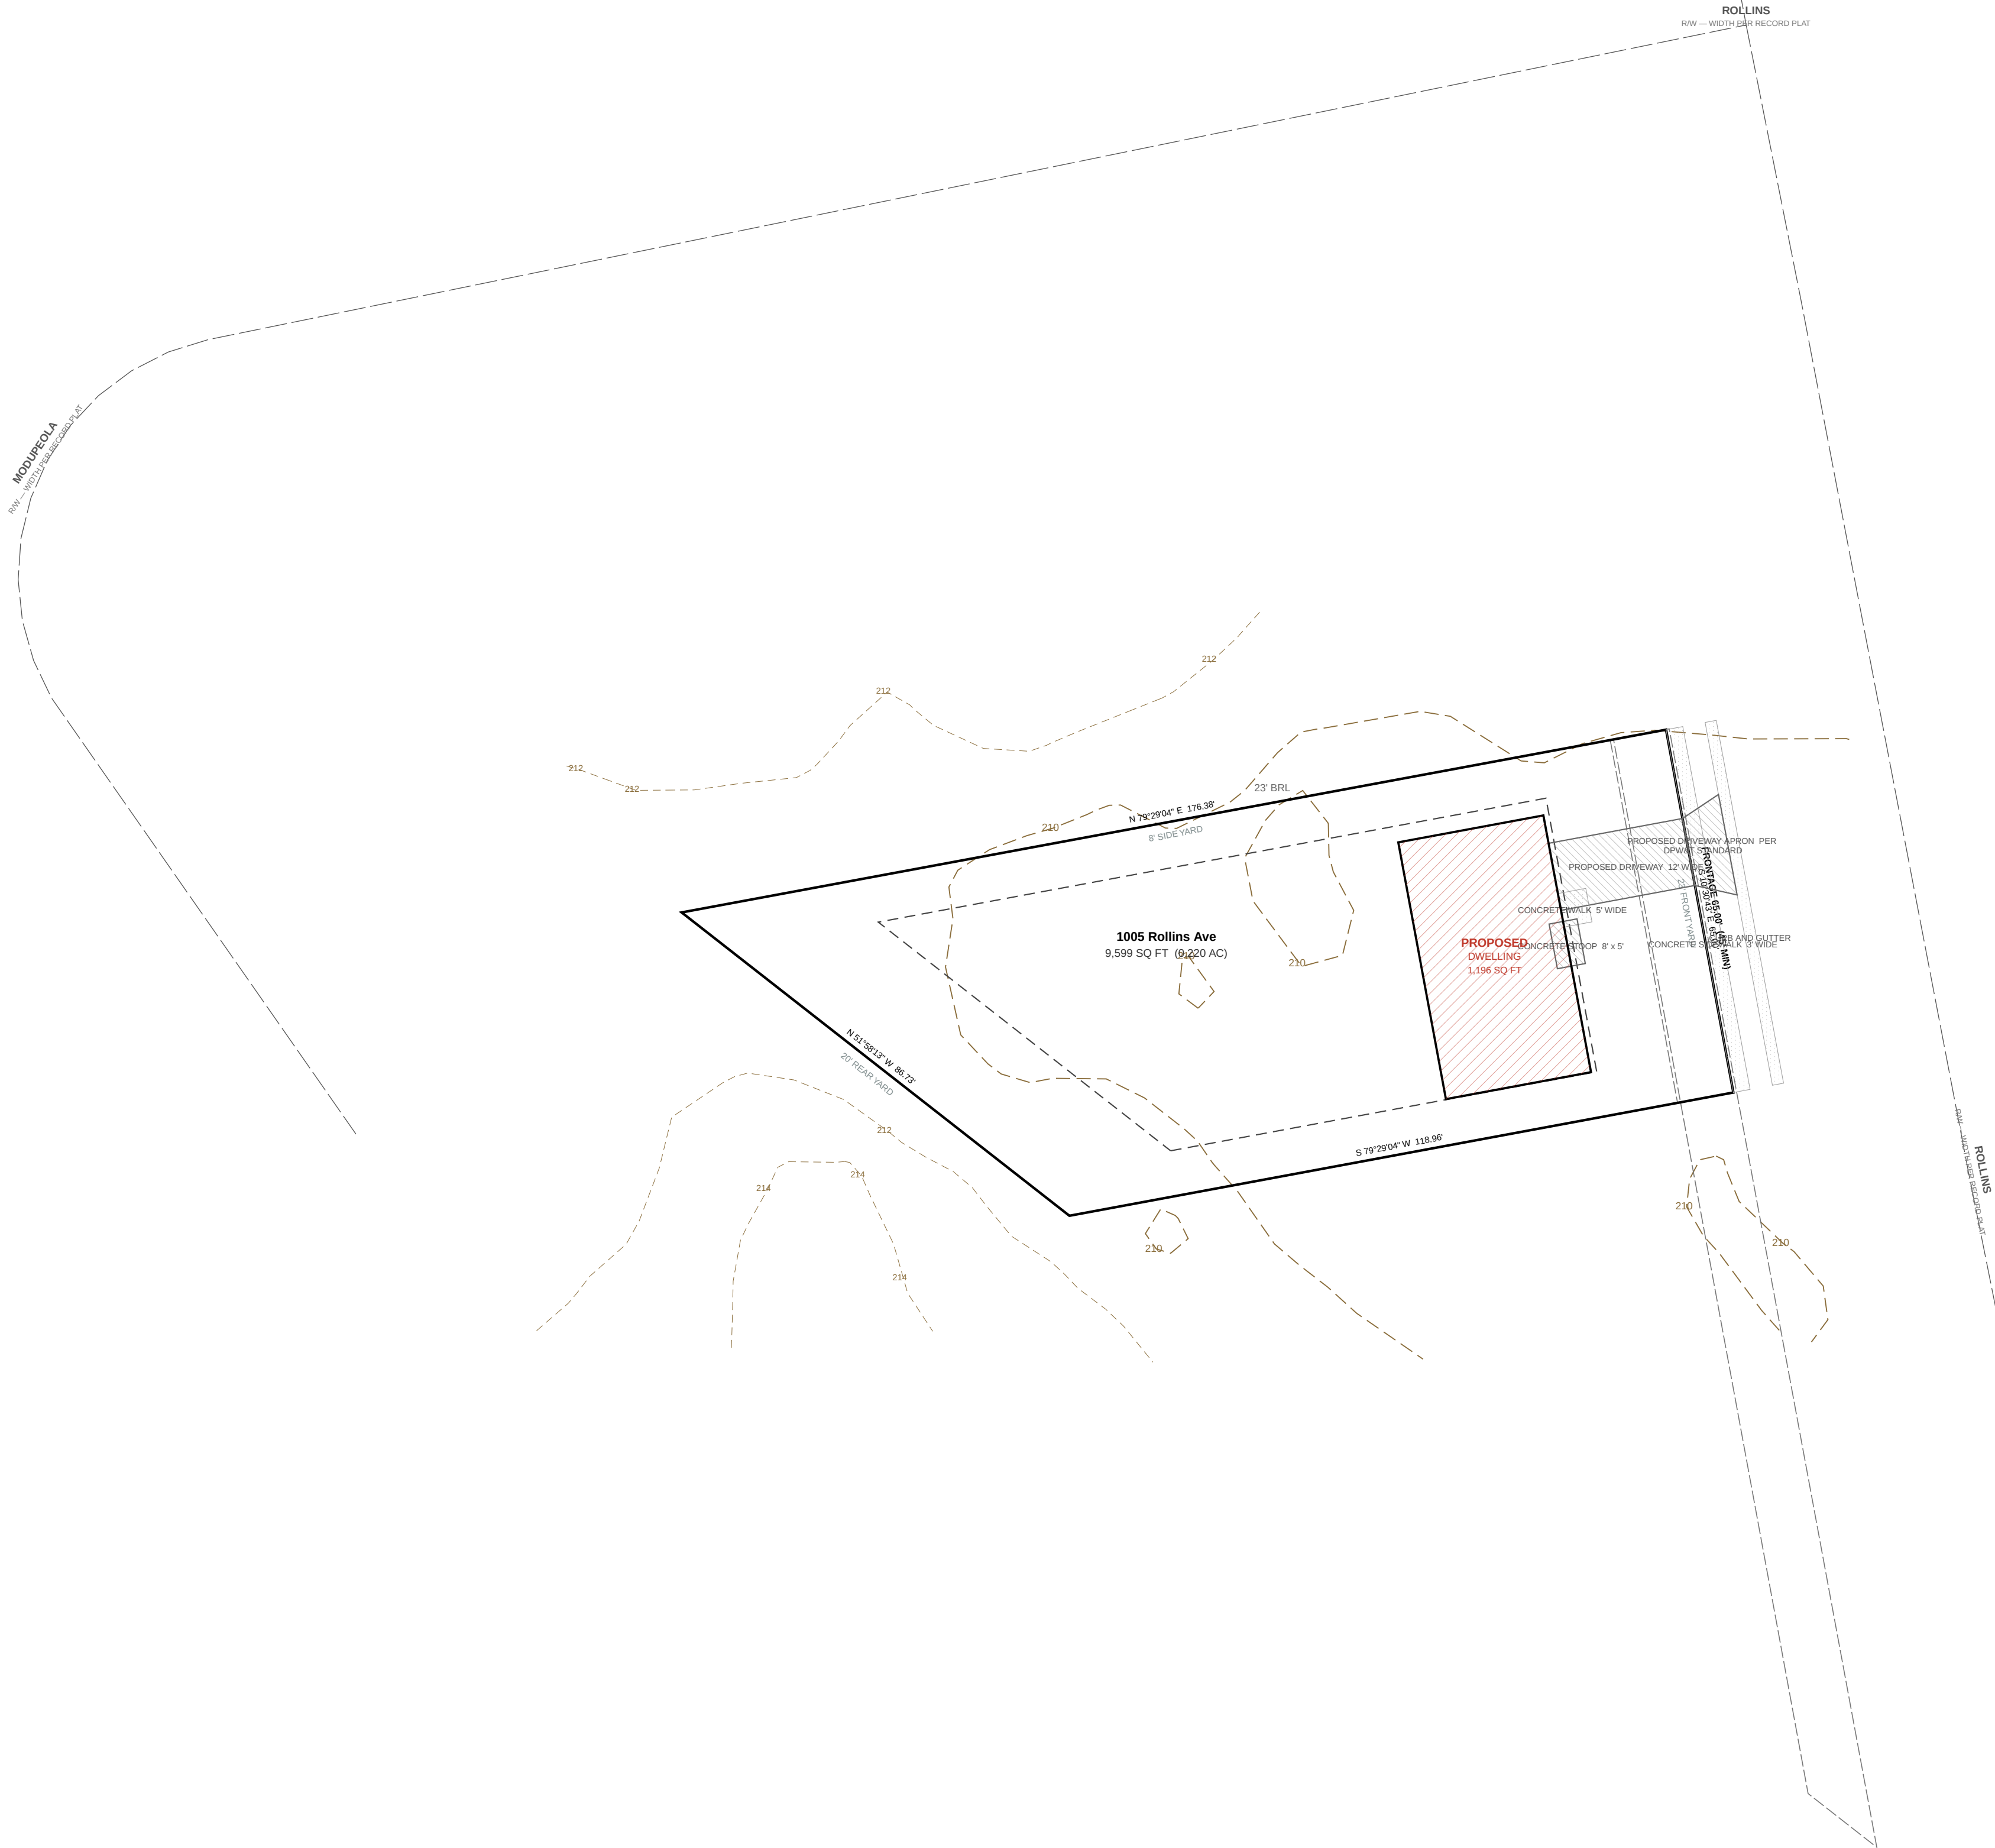

KEALEE

design, build, deliver

PROJECT

1005 Rollins Ave

ADDRESS

1005 Rollins Ave

JURISDICTION

prince georges md

ZONE

RSF-65

SHEET

C-700 — Sediment and Erosion Control Plan

SCALE

1" = 20'

STATUS

PRELIMINARY

SHEET NO.

5 OF 6

COORDINATES

EPSG:2248

H: NAD83

V: NAVD83 (feet)

SITE DATA		
ZONE	RSF-65	
TAXI PARCEL ID	1005 Rollins Ave	
GROSS LOT AREA	9,599 SF	0.220 AC
LOT FRONTAGE	45' MIN	65.00'
SETBACKS	REQUIRED	PROVIDED
FRONT YARD	23'	23'
SIDE YARD	8'	8'
REAR YARD	20'	20'
COVERAGE	MAX	PROPOSED
LOT COVERAGE	35%	12.5%
BUILDING FOOTPRINT	—	1,196 SF
DATA		
HORIZONTAL	EPSG:2248	NAD83
VERTICAL	NAVD83 (feet)	

SITE ANALYSIS	
1. Gross tract area	9,599 SF
2. Area of dwelling	1,196 SF
3. Wooded area	NOT ESTABLISHED
4. Floodplain area	NOT ESTABLISHED
5. Net tract area	9,599 SF
6. TOTAL AREA DISTURBED	NOT QUANTIFIED

SEQUENCE OF CONSTRUCTION	
1. Pre-construction meeting	1 DAY
2. Obtain necessary permits	2 DAYS
3. Notify Miss Utility at 811 at least 48 hours prior to any excavation	1 DAY
4. Construct stabilized construction entrance and perimeter sediment control	2 DAYS
5. Rough grade; construct dwelling, utilities and driveway	12 MONTHS
6. Fine grade and stabilize all disturbed areas	1 DAY
7. Remove sediment control devices when written permission has been granted	1 DAY
TOTAL ESTIMATED TIME OF CONSTRUCTION: 12 MONTHS	

GENERAL NOTES

- CONTRACTOR SHALL CONTACT MISS UTILITY AT 811 A MINIMUM OF 48 HOURS PRIOR TO ANY EXCAVATION. FIELD VERIFY LOCATION AND DEPTH BY TEST PIT BEFORE CONSTRUCTION.
- ALL EXISTING AND PROPOSED UTILITIES SHOWN PER PG CODE SEC. 32.106.
- PROPOSED GRADE SHOWN SOLID. EXISTING GRADE SHOWN DASHED.
- ROUGH EARTHWORK GRADES AND UTILITY ELEVATIONS SHOWN TO TENTHS OF A FOOT.
- BOUNDARY SHOWN IS THE RECORDED PLAT OF SUBDIVISION — PORTER SUBDIVISION, PLAT BOOK PM 231 p.50 — TRANSCRIBED AND CHECKED FOR CLOSURE. THE PLAT IS THE BOUNDARY SURVEY. NO FIELD TOPOGRAPHY IS INCLUDED. EXISTING GRADE IS COUNTY LIDAR CONTOUR MAPPING.
- CONNECT TO EXISTING PAVEMENT, CURB AND GUTTER, DRIVEWAY AND SIDEWALK IN LINE AND GRADE.

PLAT OF RECORD

Porter Subdivision, Plat Book PM 231 p.50

NOTES OF RECORD

- BASED ON RECORDED Maryland State Plane Coordinate System (NAD 83).
- BOUNDARY OF RECORD transcribed from the recorded plat; traverse closes 1.84327', 9599 SF computed against 9,599 SF recorded.
- A transcription is not a field survey. Monumentation is not verified here.

The surveyor certifies, under declaration and approval signatures of the recorded plat are NOT reproduced here; they exist in the electronic plat to this drawing.

LEGEND	
— — — — —	PROPERTY BOUNDARY
- - - - -	BRL — BUILDING RESTRICTION LINE
— — — — —	PROPOSED STRUCTURE
— — — — —	EXISTING CONTOUR — PGATLAS 2 FT (2023), NAVD83
- - - - -	STREET CENTRELINE
— — — — —	PROPOSED PAVEMENT — DRIVEWAY / WALK
- - - - -	EASEMENT

PRINCE GEORGE'S COUNTY SOIL CONSERVATION DISTRICT APPROVAL

SEDIMENT CONTROL, CRACKING, SOLS & DRAINAGE	
SIGNATURE	DATE

DPE STEREOAD PLAN REVIEW DIVISION APPROVAL

SIGNATURE	DATE
-----------	------

STABILIZATION COMPLIANCE PREAMBLE

Stabilization practices on all projects must be in compliance with the requirements of COMAR 26.17.01 by January 9, 2013, regardless of when an erosion and sediment control plan was approved.

COMAR 26.17.01.02(2), Generalization of approved plans


STANDARD STABILIZATION NOTE


Following initial soil disturbance or re-disturbance, permanent or temporary stabilization must be completed within a) Three (3) calendar days up to the surface of all perimeter ditches, swales, ditches, perimeter slopes, and all slopes steeper than 3 horizontal to 1 vertical (3:1); and b) Seven (7) calendar days up to all other disturbed or graded areas on the project site not under active grading.

2011 Maryland Standards and Specifications for Soil Erosion and Sediment Control, "Standard Stabilization Note" (adopted by COMAR 26.17.01.02(2)(A)(C))

REVISIONS

— NONE —



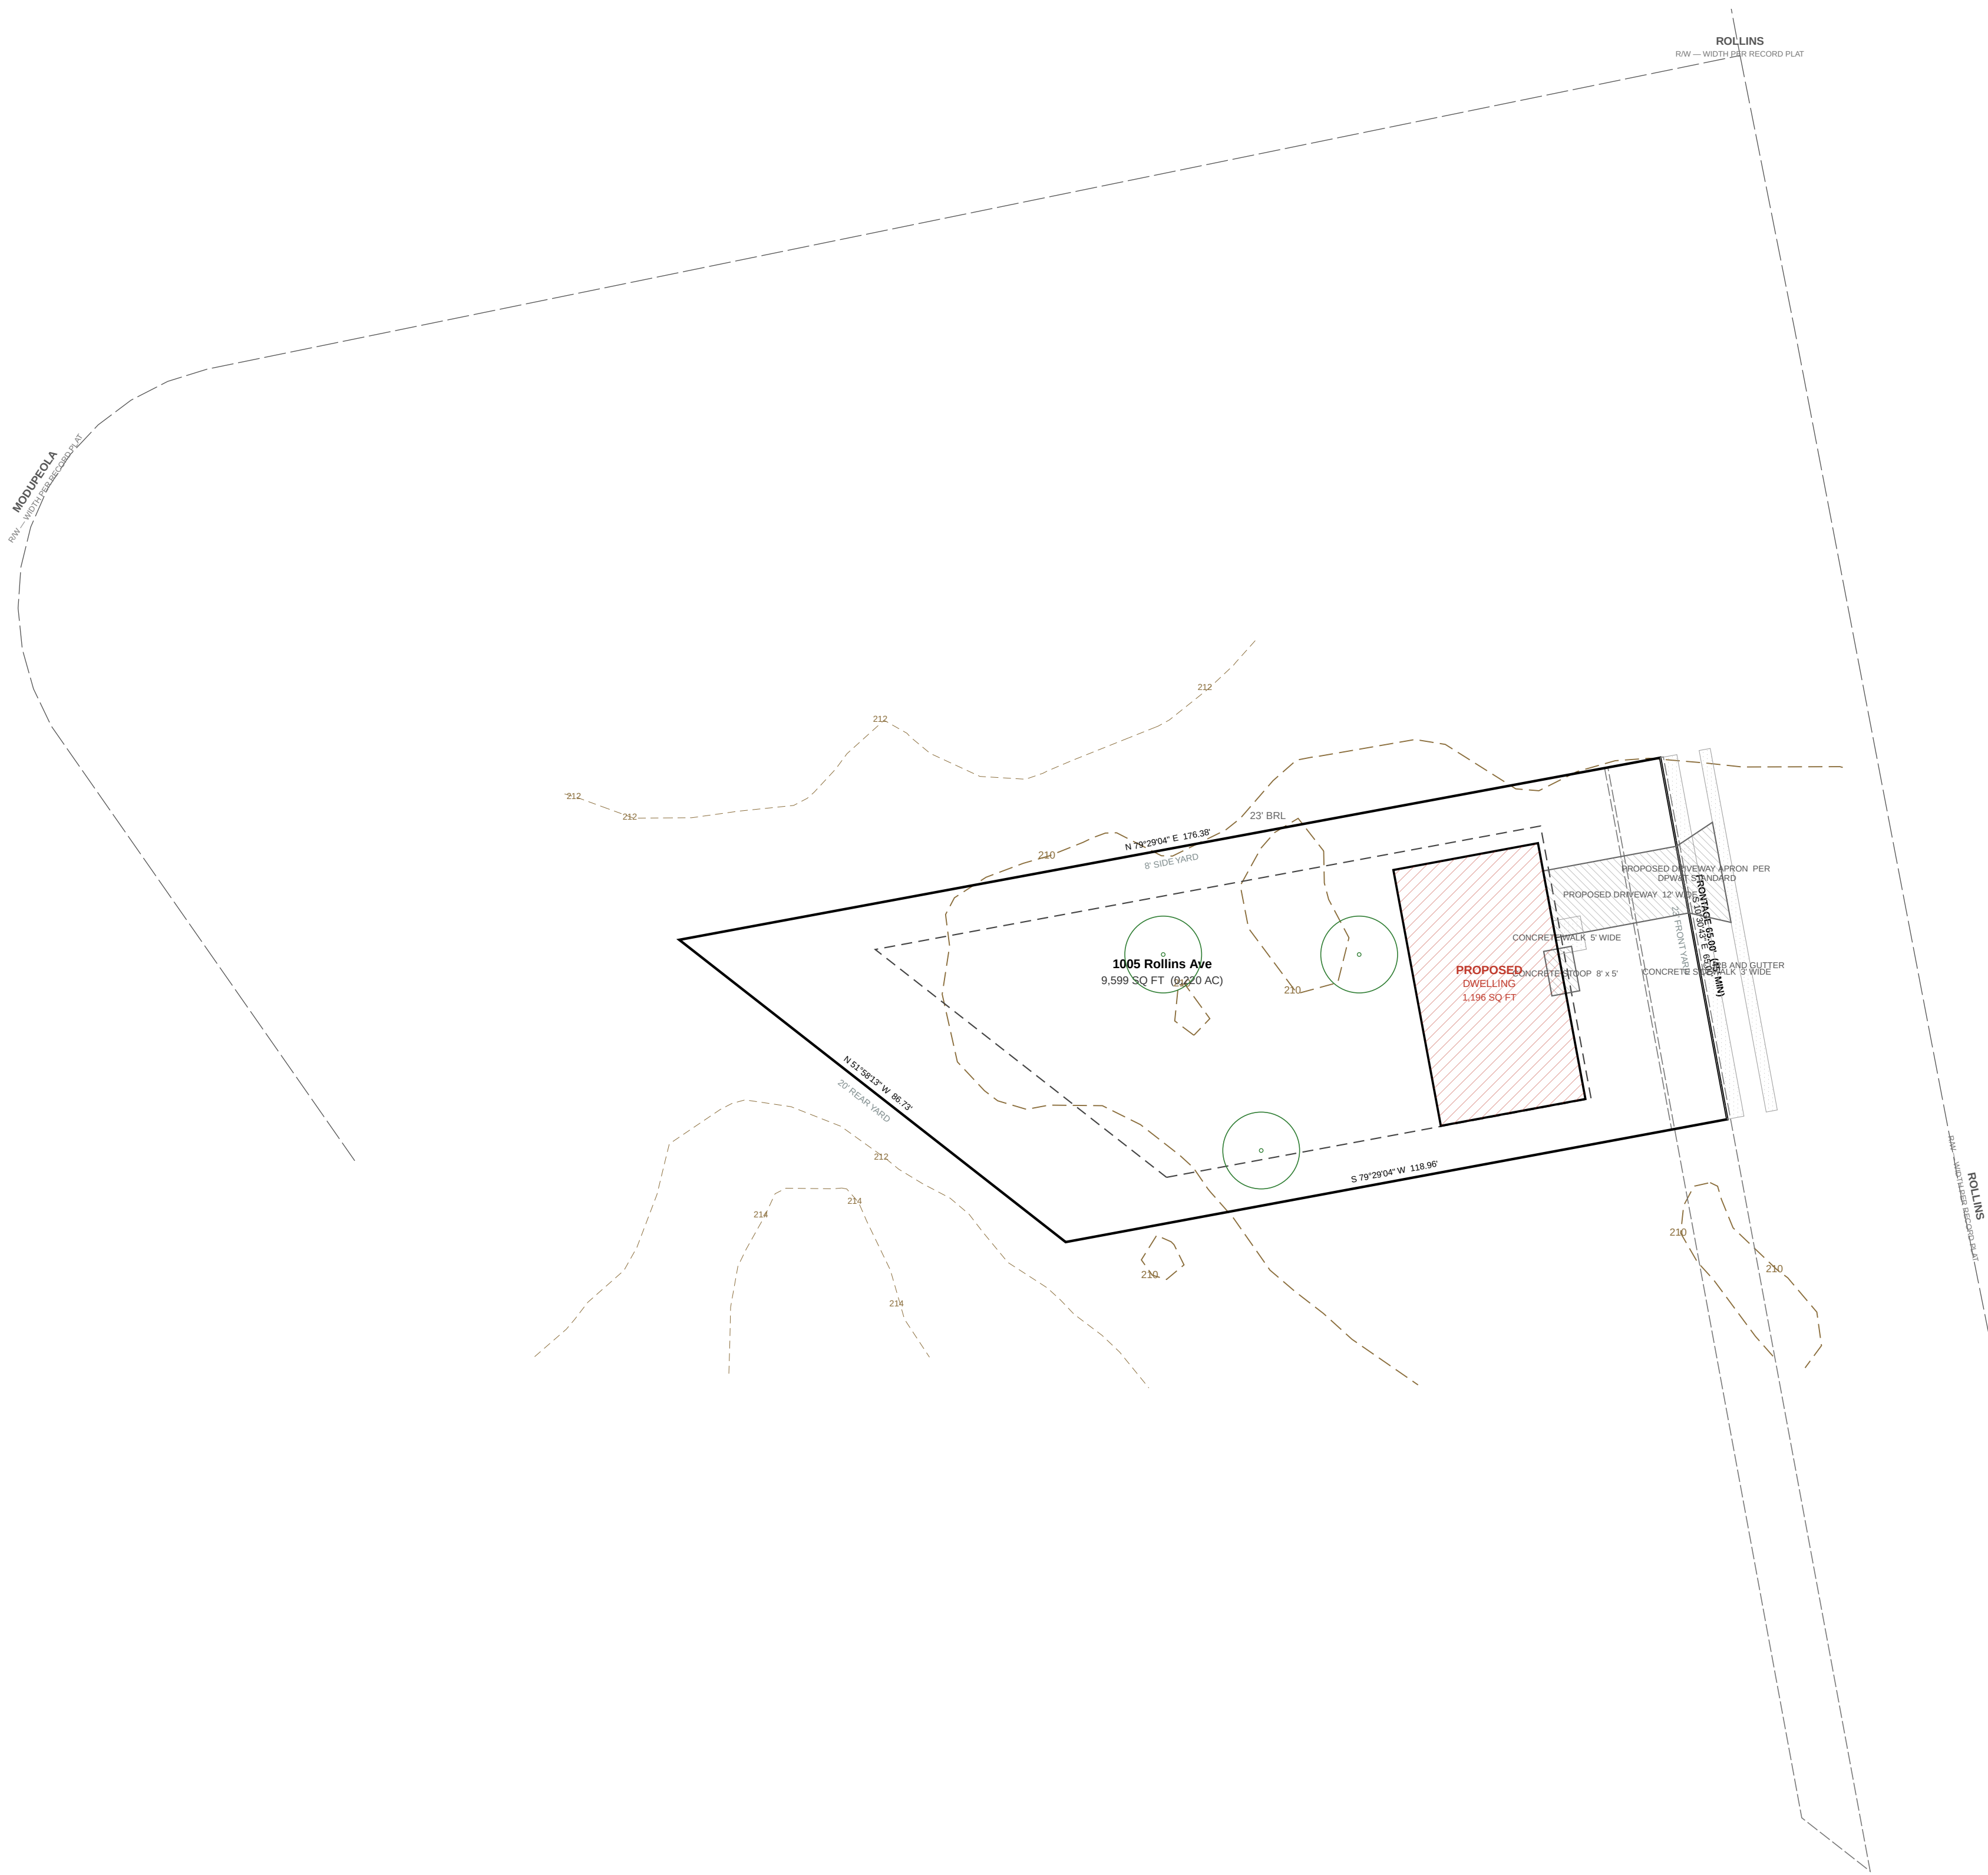

KEALEE
design, build, deliver

PROJECT
1005 Rollins Ave
ADDRESS
1005 Rollins Ave
JURISDICTION
prince georges md
ZONE
RSF-65
SHEET
L-100 — Landscape and Tree Canopy Plan
SCALE
1" = 20'
STATUS
PRELIMINARY
SHEET NO.
6 OF 6
COORDINATES
EPSG:2248
H: NAD83
V: NAVD83 (feet)

SITE DATA		
ZONE	RSF-65	
TAX PARCEL ID	1005 Rollins Ave	
GROSS LOT AREA	9,599 SF	0.220 AC
LOT FRONTAGE	45' MIN	65.00'
SETBACKS	REQUIRED	PROVIDED
FRONT YARD	23'	23'
SIDE YARD	8'	8'
REAR YARD	20'	20'
COVERAGE	MAX	PROPOSED
LOT COVERAGE	35%	12.5%
BUILDING FOOTPRINT	—	1,196 SF
DATA		
HORIZONTAL	EPSG:2248	NAD83
VERTICAL	NAVD83 (feet)	

SITE ANALYSIS	
1. Gross lot area	9,599 SF
2. Area of dwelling	1,196 SF
3. Wooded area	NOT ESTABLISHED
4. Floodplain area	NOT ESTABLISHED
5. Net lot area	9,599 SF
6. TOTAL AREA DISTURBED	NOT QUANTIFIED

SEQUENCE OF CONSTRUCTION	
1. Pre-construction meeting	1 DAY
2. Obtain necessary permits	2 DAYS
3. Notify M&D Utility at 811 at least 48 hours prior to any excavation	1 DAY
4. Construct stabilized construction entrance and perimeter sediment control	2 DAYS
5. Rough grade, construct dwelling, utilities and driveway	12 MONTHS
6. Fine grade and stabilize all disturbed areas	1 DAY
7. Remove sediment control devices when written permission has been granted	1 DAY
TOTAL ESTIMATED TIME OF CONSTRUCTION: 12 MONTHS	

GENERAL NOTES

- CONTRACTOR SHALL CONTACT MISS UTILITY AT 811 A MINIMUM OF 48 HOURS PRIOR TO ANY EXCAVATION. FIELD VERIFY LOCATION AND DEPTH BY TEST PIT BEFORE CONSTRUCTION.
- ALL EXISTING AND PROPOSED UTILITIES SHOWN PER PG&E CODE SEC. 32.106.
- PROPOSED GRADE SHOWN SOLID EXISTING GRADE SHOWN DASHED.
- ROUGH EARTHWORK GRADES AND UTILITY ELEVATIONS SHOWN TO TENTHS OF A FOOT.
- BOUNDARY SHOWN IS THE RECORDED PLAT OF SUBDIVISION — PORTER SUBDIVISION, PLAT BOOK PM 231 P.50 — TRANSCRIBED AND CHECKED FOR CLOSURE. THE PLAT IS THE BOUNDARY SURVEY. NO FIELD TOPOGRAPHY IS INCLUDED. EXISTING GRADE IS COUNTY LIDAR CONTOUR MAPPING.
- CONNECT TO EXISTING PAVEMENT, CURB AND GUTTER, DRIVEWAY AND SIDEWALK IN LINE AND GRADE.

PLAT OF RECORD

Porter Subdivision, Plat Book PM 231 p.50

NOTES OF RECORD

- BASED ON: GEOMETRIC Maryland State Plane Coordinate System (NAD 83).
- BOUNDARY OF RECORD transcribed from the recorded plat; traverse closes 1.84327, 9599 SF computed against 9,599 SF recorded.
- A transcription is not a field survey. Monumentation is not verified here.

The surveyor certifies, under declaration and approval signatures of the recorded plat are NOT reproduced here; they shall be the responsibility of the client.

LEGEND

- PROPERTY BOUNDARY
- BRL — BUILDING RESTRICTION LINE
- PROPOSED STRUCTURE
- EXISTING CONTOUR — PG&E 2 FT (2023), NAVD83
- STREET CENTRELINE
- PROPOSED PAVEMENT — DRIVEWAY / WALK
- EASEMENT

PRINCE GEORGE'S COUNTY SOL CONSERVATION DISTRICT APPROVAL

SEDIMENT CONTROL, CRACKING, SOLS & DRAINAGE

SIGNATURE	DATE
-----------	------

DPE SITEROAD PLAN REVIEW DIVISION APPROVAL

SIGNATURE	DATE
-----------	------

REVISIONS

— NONE —

