



KEALEE

Design, build, deliver

PROJECT
111 MARYLAND AVE
ADDRESS
111 MARYLAND AVE
JURISDICTION
City of Rockville, Maryland
ZONE

SHEET
C-100 — Existing Conditions and Boundary Plan
SCALE
1" = 30'
STATUS
PRELIMINARY
SHEET NO.
1 OF 5
COORDINATES
EPSG-2248
H: NAD83
V: NAVD88 (feet)

PROFESSIONAL RESPONSIBILITY
Maryland Licensed Surveyor
certifies: boundary_determination, topographic_survey

SEAL AND SIGNATURE

All content on this sheet falls within one professional scope.

PLAN TYPE AND PREPARATION

PLANTYPE SITE DEVELOPMENT / FINE GRADING
SHEET C-100 — Existing Conditions and Boundary Plan
DISCIPLINE Maryland Licensed Surveyor
DRAWN BY KEALEE SITE-PLAN ENGINE
DESIGNED BY
CHECKED BY

REVISIONS

NO.	DATE	DESCRIPTION

SITE DATA

ZONE	
TAX / PARCEL ID	00150968
GROSS TRACT AREA	31,197 SF 0.716 AC
LOT FRONTAGE	— 143.71'
SETBACKS	REQUIRED PROVIDED
FRONT YARD	— —
SIDE YARD	— —
REAR YARD	— —
COVERAGE	MAX PROPOSED
LOT COVERAGE	— 3.8%
BUILDING FOOTPRINT	— 1,200 SF
DATUM	
HORIZONTAL	EPSG-2248 NAD83
VERTICAL	NAVD88 (feet)

SITE ANALYSIS

1. Gross tract area	31,197 SF
2. Area of dwelling	1,200 SF
3. Wooded area	NOT ESTABLISHED
4. Floodplain area	NOT ESTABLISHED
5. Net lot area	31,197 SF
6. TOTAL AREA DISTURBED	7,073 SF (AT LEAST)
7. SWM REVIEW	CONFIRM WITH CITY OF ROCKVILLE

BUILDING DATA

	G	B	FF	SF	HT	STY
111 MARYLAND AVE	—	—	—	—	20'	2

G: garage slab; B: basement; FF: finished floor; SF: subfloor; HT: height; STY: storeys. A DASH IS NOT ZERO: the elevation has not been established and must be set from a field-run topographic survey before construction.

DRAINAGE AREA COMPUTATIONS

CATCHMENT	SF	ACRES	C
Total — 4.4% Impervious	31,197	0.716	
PRE-DEVELOPMENT	SF		C
Pervious — lawn / meadow	31,197		0.25
Composite C			0.250
POST-DEVELOPMENT	SF		C
Proposed roof	1,200		0.95
Driveway and on-lot paving	177		0.95
Pervious — lawn	29,820		0.25
Composite C			0.281
Flow path	298 ft		
Flow path slope	6.0 %		
Time of concentration (Kirpich)	5.0 min		
Rainfall intensity, 10-yr	6.60 in/hr		
Peak discharge PPE, Q = CIA	1.18 cfs		
Peak discharge POST, Q = CIA	1.33 cfs		
INCREASE TO BE MANAGED	0.15 cfs		
Rv = 0.05 + 0.0091	0.0897		
Water quality volume Wqv	233 cf		

Time of concentration by Kirpich over a 298 ft flow path at 6.0%, taken from the 2 ft contours across the catchment. A 5-minute floor applies.
Rainfall intensity 6.60 in/hr for the 10-year storm at a 5.0 minute duration, NOAA Atlas 14 Vol. 2 Ver. 3, PFDS point estimate, 39.0817 N 77.1516 W.
Water quality volume on a 1.0 in rainfall, Maryland Stormwater Design Manual, Vol. 1 & 2 — WQV on a 1.0 in rainfall.
Runoff coefficients: roof and pavement 0.95, average lawn 0.25. Confirm the lawn coefficient against the soil hydrologic group before relying on the composite.
Sidewalk, curb and gutter and the driveway apron lie in the public right-of-way and drain to the street. They are excluded from the lot catchment and included in the disturbed areas.

SEQUENCE OF CONSTRUCTION

1. Pre-construction meeting
2. Obtain necessary permits
3. Notify Miss Utility at 811 at least 48 hours prior to any excavation
4. Install stabilized construction entrance and perimeter sediment control
5. Rough grade the lot
6. Construct dwelling
7. Install water, sewer and storm services and the driveway
8. Fine grade and stabilize all disturbed areas
9. Remove sediment control once the inspector gives written permission

TOTAL ESTIMATED TIME OF CONSTRUCTION: 8 MONTHS

GENERAL NOTES

1. CONTRACTOR SHALL CONTACT MISS UTILITY AT 811 A MINIMUM OF 48 HOURS PRIOR TO ANY EXCAVATION. FIELD-VERIFY LOCATION AND DEPTH BY TEST PIT BEFORE CONSTRUCTION.
2. EXISTING UTILITIES ARE SHOWN FROM PUBLIC RECORD AND ARE APPROXIMATE. LOCATION AND DEPTH SHALL BE FIELD-VERIFIED BY TEST PIT BEFORE CONSTRUCTION.
3. PROPOSED GRADE SHOWN SOLID; EXISTING GRADE SHOWN DASHED.
4. ROUGH EARTHWORK GRADES AND UTILITY ELEVATIONS SHOWN TO TENTHS OF A FOOT.
5. BOUNDARY SHOWN IS COMPILED JURISDICTION GIS, NOT A BOUNDARY SURVEY.
6. CONNECT TO EXISTING PAVEMENT, CURB AND GUTTER, DRIVEWAY AND SIDEWALK IN LINE AND GRADE.
7. NO DRIVEWAY CULVERT IS REQUIRED. THIS FRONTAGE IS AN EXISTING CURB AND GUTTER SECTION. NOT AN OPEN DITCH SECTION. GUTTER FLOW IS CARRIED THROUGH EACH ENTRANCE BY THE DEPRESSED CURB AT THE APRON PER CITY OF ROCKVILLE STANDARD. ONLY LOT DRAINAGE IS COLLECTED BY THE REAR-YARD SWALE IN THE REAR DRAINAGE EASEMENT AND CROSSES NO DRIVEWAY OR APRON.

PROFESSIONAL CERTIFICATION

I HEREBY CERTIFY THAT THESE DOCUMENTS WERE PREPARED OR APPROVED BY ME, AND THAT I AM A DULY LICENSED PROFESSIONAL ENGINEER UNDER THE LAWS OF THE STATE OF MARYLAND.

SIGNATURE DATE

SEAL LICENSE NO. EXPIRATION DATE

REVISIONS

— NONE —

SOILS TABLE USDA NRCS SSURGO

MAP UNIT	MAP UNIT NAME	K-FACT	HYDRIC	HYD. GRP	DRAINAGE CLASS
100	Dumps, refuse	—	No	—	
109D	Hyattstown channery silt loam, 15 to 25 percent slopes, very	.49	No	D	Well drained
109E	Hyattstown channery silt loam, 25 to 45 percent slopes, very	.49	No	D	Well drained
116C	Blocktown channery silt loam, 8 to 15 percent slopes, very	.49	No	D	Well drained
116D	Blocktown channery silt loam, 15 to 25 percent slopes, very	.49	No	D	Well drained
116E	Blocktown channery silt loam, 25 to 45 percent slopes, very	.49	No	D	Well drained
16B	Blocktown channery silt loams, 3 to 8 percent slopes	.43	No	C	Well drained

SOURCE AND ACCURACY
Parcel boundary — Jurisdiction gis — M-NCPPC Montgomery Planning — parcels (SDAT) — level 1
Existing contours — M-NCPPC Montgomery Planning — backgrounds/Contours_28/MapServer/1 — Contours (. . .

GRAPHIC SCALE — 1" = 30'





KEALEE

Design, build, deliver

PROJECT
111 MARYLAND AVE
ADDRESS
111 MARYLAND AVE
JURISDICTION
City of Rockville, Maryland
ZONE

SHEET
C-200 — Overall Site and Zoning Plan
SCALE
1" = 30'

STATUS
PRELIMINARY
SHEET NO.
2 OF 5

COORDINATES
EPSG:2248
H: NAD83
V: NAVD88 (feet)

PROFESSIONAL RESPONSIBILITY
Maryland Professional Engineer
certifies: site, layout

SEAL AND SIGNATURE

Architect
certifies: architectural_footprint

SEAL AND SIGNATURE

This sheet carries content from more than one professional discipline. Each seal below applies only to the subjects listed beside it. No professional certifies content outside their stated scope, and the sheet is not divided into separate drawings for that purpose.

PLAN TYPE AND PREPARATION

PLANTYPE SITE DEVELOPMENT / FINE GRADING
SHEET C-200 — Overall Site and Zoning Plan
DISCIPLINE Maryland Professional Engineer
DRAWN BY KEALEE SITE-PLAN ENGINE
DESIGNED BY
CHECKED BY

REVISIONS

NO.	DATE	DESCRIPTION

SITE DATA

ZONE	
TAX / PARCEL ID	00150968
GROSS TRACT AREA	31,197 SF 0.716 AC
LOT FRONTAGE	143.71'
SETBACKS	REQUIRED PROVIDED
FRONT YARD	— —
SIDE YARD	— —
REAR YARD	— —
COVERAGE	MAX PROPOSED
LOT COVERAGE	— 3.8%
BUILDING FOOTPRINT	— 1,200 SF
DATUM	
HORIZONTAL	EPSG:2248 NAD83
VERTICAL	NAVD88 (feet)

SITE ANALYSIS

1. Gross tract area	31,197 SF
2. Area of dwelling	1,200 SF
3. Wooded area	NOT ESTABLISHED
4. Floodplain area	NOT ESTABLISHED
5. Net lot area	31,197 SF
6. TOTAL AREA DISTURBED	7,073 SF (AT LEAST)
7. SWM REVIEW	CONFIRM WITH CITY OF ROCKVILLE

BUILDING DATA

	G	B	FF	SF	HT	STY
111 MARYLAND AVE	—	—	—	—	20'	2

G: garage slab - B: basement - FF: finished floor - SF: subfloor - HT: height - STY: storeys. A DASH IS NOT ZERO; the elevation has not been established and must be set from a field-run topographic survey before construction.

DRAINAGE AREA COMPUTATIONS

CATCHMENT	SF	ACRES	C
Total — 4.4% impervious	31,197	0.716	
PRE-DEVELOPMENT	SF		C
Pervious — lawn / meadow	31,197		0.25
Composite C			0.250
POST-DEVELOPMENT	SF		C
Proposed roof	1,200		0.95
Driveway and on-roof paving	177		0.95
Pervious — lawn	29,820		0.25
Composite C			0.281
Flow path			298 ft
Flow path slope			8.0 %
Time of concentration (Kirpich)			5.0 min
Rainfall intensity, 10-yr			6.60 in/hr
Peak discharge PHE, Q = CIA			1.18 cfs
Peak discharge POST, Q = CIA			1.33 cfs
INCREASE TO BE MANAGED			0.15 cfs
Rv = 0.05 + 0.008 I			0.0897
Water quality volume WQv			233 cf

Time of concentration by Kirpich over a 298 ft flow path at 6.0%, taken from the 2 ft contours across the catchment. A 5-minute flow applies.
Rainfall intensity 6.60 in/hr for the 10-year storm at a 5.0 minute duration, NOAA Atlas 14 Vol. 2 ver. 3, PFDS point estimate, 39.0817 N 77.1516 W.
Water quality volume on a 1.0 in rainfall, Maryland Stormwater Design Manual, Vol. 1 & 2 — WQv on a 1.0 in rainfall.
Runoff coefficients: roof and pavement 0.95, average lawn 0.25. Confirm the lawn coefficient against the soil hydrologic group before relying on the composite.
Sidewalk, curb and gutter and the driveway apron lie in the public right-of-way and drain to the street. They are excluded from the lot catchment and included in the disturbed area.

SEQUENCE OF CONSTRUCTION

1. Pre-construction meeting	1 DAY
2. Obtain necessary permits	2 DAYS
3. Notify Miss Utility at 811 at least 48 hours prior to any excavation	1 DAY
4. Install stabilized construction entrance and perimeter sediment control	2 DAYS
5. Rough grade the lot	5 DAYS
6. Construct dwelling	6 MONTHS
7. Install water, sewer and storm services and the driveway	10 DAYS
8. Fine grade and stabilize all disturbed areas	5 DAYS
9. Remove sediment control once the inspector gives written permission	1 DAY
TOTAL ESTIMATED TIME OF CONSTRUCTION: 8 MONTHS	

LEGEND

- PROPERTY BOUNDARY
- BRL — BUILDING RESTRICTION LINE
- PROPOSED STRUCTURE
- EXISTING CONTOUR — 2 FT INTERVAL, NAVD88
- PROPOSED CONTOUR — 2 FT INTERVAL
- STREET CENTRELINE
- PROPOSED PAVEMENT — DRIVEWAY / WALK
- EASEMENT
- SANITARY LATERAL (SHC) — HEAVIEST
- WATER SERVICE (WNC)
- STORM DRAIN — TRUNK, RCP
- STORM — HOUSE CONNECTION TO TRUNK
- DRAINAGE SWALE — INVERT AND GRADED SECTION
- RETAINING WALL — TICKS ON THE RETAINED SIDE
- LIMIT OF GROUND COVER — TICKS ON THE STEEP SIDE
- ESD — STORMWATER PRACTICE

PROFESSIONAL CERTIFICATION

I HEREBY CERTIFY THAT THESE DOCUMENTS WERE PREPARED OR APPROVED BY ME, AND THAT I AM A DULY LICENSED PROFESSIONAL ENGINEER UNDER THE LAWS OF THE STATE OF MARYLAND.

SIGNATURE

DATE

SEAL

LICENSE NO.

EXPIRATION DATE

REVISIONS

— NONE —

SOILS TABLE

USDA NRCS SSURGO

MAP UNIT	MAP UNIT NAME	K-FACT	HYDRIC	HYD. GRP	DRAINAGE CLASS
100	Dumps, refuse	—	No	—	—
109D	Hyattstown channery silt loam, 15 to 25 percent slopes, very	.49	No	D	Well drained
109E	Hyattstown channery silt loam, 25 to 45 percent slopes, very	.49	No	D	Well drained
116C	Blacktown channery silt loam, 8 to 15 percent slopes, very	.49	No	D	Well drained
116D	Blacktown channery silt loam, 15 to 25 percent slopes, very	.49	No	D	Well drained
116E	Blacktown channery silt loam, 25 to 45 percent slopes, very	.49	No	D	Well drained
16B	Blacktown channery silt loams, 3 to 8 percent slopes	.43	No	C	Well drained

SOURCE AND ACCURACY
Parcel boundary — Jurisdiction gis — M-NCPPC Montgomery Planning — parcels (SDAT) — level 1
Existing contours — M-NCPPC Montgomery Planning — backgrounds/Contours_28/MapServer/1 — Contours (...

GRAPHIC SCALE — 1" = 30'

0 30 60 90 120 FEET



KEALEE

Design, build, deliver

PROJECT
111 MARYLAND AVE
ADDRESS
111 MARYLAND AVE
JURISDICTION
City of Rockville, Maryland
ZONE

SHEET
C-400 — Grading and Drainage Plan
SCALE
1" = 30'
STATUS
PRELIMINARY
SHEET NO.
3 OF 5
COORDINATES
EPSG:2248
H: NAD83
V: NAVD88 (feet)

PROFESSIONAL RESPONSIBILITY
Maryland Professional Engineer
certifies: grading_design, sediment_control, stormwater_design

SEAL AND SIGNATURE

All content on this sheet falls within one professional scope.

PLAN TYPE AND PREPARATION

PLAN TYPE SITE DEVELOPMENT / FINE GRADING
SHEET C-400 — Grading and Drainage Plan
DISCIPLINE Maryland Professional Engineer
DRAWN BY KEALEE SITE-PLAN ENGINE
DESIGNED BY
CHECKED BY

REVISIONS

NO.	DATE	DESCRIPTION

SITE DATA

ZONE	
TAX / PARCEL ID	00150968
GROSS TRACT AREA	31,197 SF 0.716 AC
LOT FRONTAGE	— 143.71'
SETBACKS	REQUIRED PROVIDED
FRONT YARD	— —
SIDE YARD	— —
REAR YARD	— —
COVERAGE	MAX PROPOSED
LOT COVERAGE	— 3.8%
BUILDING FOOTPRINT	— 1,200 SF
DATUM	
HORIZONTAL	EPSG:2248 NAD83
VERTICAL	NAVD88 (feet)

SITE ANALYSIS

1. Gross tract area	31,197 SF
2. Area of dwelling	1,200 SF
3. Wooded area	NOT ESTABLISHED
4. Floodplain area	NOT ESTABLISHED
5. Net lot area	31,197 SF
6. TOTAL AREA DISTURBED	7,073 SF (AT LEAST) CONFIRM WITH CITY OF ROCKVILLE
7. SWM REVIEW	

BUILDING DATA

	G	B	FF	SF	HT	STY
111 MARYLAND AVE	—	—	—	—	20'	2

G: garage slab; B: basement; FF: finished floor; SF: subfloor; HT: height; STY: storeys. A DASH IS NOT ZERO: the elevation has not been established and must be set from a field-run topographic survey before construction.

DRAINAGE AREA COMPUTATIONS

CATCHMENT	SF	ACRES	C
Total — 4.4% impervious	31,197	0.716	
PRE-DEVELOPMENT	SF		C
Pervious — lawn / meadow	31,197		0.25
Composite C			0.250
POST-DEVELOPMENT	SF		C
Proposed roof	1,200		0.95
Driveway and on-lot paving	177		0.95
Pervious — lawn	29,820		0.25
Composite C			0.281
Flow path	298 ft		
Flow path slope	6.0 %		
Time of concentration (Kirpich)	5.0 min		
Rainfall intensity, 10-yr	6.60 in/hr		
Peak discharge PRE, Q = CIA	1.18 cfs		
Peak discharge POST, Q = CIA	1.33 cfs		
INCREASE TO BE MANAGED	0.15 cfs		
Rv = 0.05 + 0.0091	0.0897		
Water quality volume WqV	233 cf		

Time of concentration by Kirpich over a 298 ft flow path at 6.0%, taken from the 2 ft contours across the catchment. A 5-minute floor applies.
Rainfall intensity 6.60 in/hr for the 10-year storm at a 5.0 minute duration, NOAA Atlas 14 Vol. 2 Ver. 3, PFDS point estimate, 39.0817 N 77.1516 W.
Water quality volume on a 1.0 in rainfall, Maryland Stormwater Design Manual, Vol. 1 & 2 — WQV on a 1.0 in rainfall.
Runoff coefficients: roof and pavement 0.95, average lawn 0.25. Confirm the lawn coefficient against the soil hydrologic group before relying on the composite.
Sewer, curb and gutter and the driveway apron lie in the public right-of-way and drain to the street. They are excluded from the lot catchment and included in the disturbed areas.

SEQUENCE OF CONSTRUCTION

1. Pre-construction meeting
2. Obtain necessary permits
3. Notify Miss Utility at 811 at least 48 hours prior to any excavation
4. Install stabilized construction entrance and perimeter sediment control
5. Rough grade the lot
6. Construct dwelling
7. Install water, sewer and storm services and the driveway
8. Fine grade and stabilize all disturbed areas
9. Remove sediment control once the inspector gives written permission

TOTAL ESTIMATED TIME OF CONSTRUCTION: 8 MONTHS

GENERAL NOTES

1. CONTRACTOR SHALL CONTACT MISS UTILITY AT 811 A MINIMUM OF 48 HOURS PRIOR TO ANY EXCAVATION. FIELD-VERIFY LOCATION AND DEPTH BY TEST PIT BEFORE CONSTRUCTION.
2. EXISTING UTILITIES ARE SHOWN FROM PUBLIC RECORD AND ARE APPROXIMATE. LOCATION AND DEPTH SHALL BE FIELD-VERIFIED BY TEST PIT BEFORE CONSTRUCTION.
3. PROPOSED GRADE SHOWN SOLID; EXISTING GRADE SHOWN DASHED.
4. ROUGH EARTHWORK GRADES AND UTILITY ELEVATIONS SHOWN TO TENTHS OF A FOOT.
5. BOUNDARY SHOWN IS COMPILED JURISDICTION GIS, NOT A BOUNDARY SURVEY.
6. CONNECT TO EXISTING PAVEMENT, CURB AND GUTTER, DRIVEWAY AND SIDEWALK IN LINE AND GRADE.
7. NO DRIVEWAY CULVERT IS REQUIRED. THIS FRONTAGE IS AN EXISTING CURB AND GUTTER SECTION, NOT AN OPEN DITCH SECTION. GUTTER FLOW IS CARRIED THROUGH EACH ENTRANCE BY THE DEPRESSED CURB AT THE APRON PER CITY OF ROCKVILLE STANDARD. ONLY LOT DRAINAGE IS COLLECTED BY THE REAR-YARD SWALE IN THE REAR DRAINAGE EASEMENT AND CROSSES NO DRIVEWAY OR APRON.

PROFESSIONAL CERTIFICATION

I HEREBY CERTIFY THAT THESE DOCUMENTS WERE PREPARED OR APPROVED BY ME, AND THAT I AM A DULY LICENSED PROFESSIONAL ENGINEER UNDER THE LAWS OF THE STATE OF MARYLAND.

SIGNATURE DATE

SEAL LICENSE NO. EXPIRATION DATE

REVISIONS

— NONE —

SOILS TABLE USDA NRCS SSURGO

MAP UNIT	MAP UNIT NAME	K-FACT	HYDRIC	HYD. GRP	DRAINAGE CLASS
100	Dumps, refuse	—	No	—	
109D	Hyattstown channery silt loam, 15 to 25 percent slopes, very	.49	No	D	Well drained
109E	Hyattstown channery silt loam, 25 to 45 percent slopes, very	.49	No	D	Well drained
116C	Blocktown channery silt loam, 8 to 15 percent slopes, very	.49	No	D	Well drained
116D	Blocktown channery silt loam, 15 to 25 percent slopes, very	.49	No	D	Well drained
116E	Blocktown channery silt loam, 25 to 45 percent slopes, very	.49	No	D	Well drained
16B	Blocktown channery silt loams, 3 to 8 percent slopes	.43	No	C	Well drained

SOURCE AND ACCURACY
Parcel boundary — Jurisdiction gis — M-NCPPC Montgomery Planning — parcels (SDAT) — level 1
Existing contours — M-NCPPC Montgomery Planning — backgrounds/Contours_28/MapServer/1 — Contours (...

GRAPHIC SCALE — 1" = 30'

0 30 60 90 120 FEET



KEALEE

Design, build, deliver

PROJECT
111 MARYLAND AVE
ADDRESS
111 MARYLAND AVE
JURISDICTION
City of Rockville, Maryland
ZONE

SHEET
C-500 — Utility Plan
SCALE
1" = 30'

STATUS
PRELIMINARY
SHEET NO.
4 OF 5

COORDINATES
EPSG-2248
H: NAD83
V: NAVD88 (feet)

PROFESSIONAL RESPONSIBILITY
Maryland Professional Engineer
certifies: Utility_Design

SEAL AND SIGNATURE

All content on this sheet falls within one professional scope.

PLAN TYPE AND PREPARATION

PLANTYPE SITE DEVELOPMENT / FINE GRADING
SHEET C-500 — Utility Plan
DISCIPLINE Maryland Professional Engineer
DRAWN BY KEALEE SITE-PLAN ENGINE
DESIGNED BY
CHECKED BY

REVISIONS

NO.	DATE	DESCRIPTION

SITE DATA

ZONE	
TAX / PARCEL ID	00150968
GROSS TRACT AREA	31,197 SF 0.716 AC
LOT FRONTAGE	— 143.71'
SETBACKS	REQUIRED PROVIDED
FRONT YARD	— —
SIDE YARD	— —
REAR YARD	— —
COVERAGE	MAX PROPOSED
LOT COVERAGE	— 3.8%
BUILDING FOOTPRINT	— 1,200 SF
DATUM	
HORIZONTAL	EPSG-2248 NAD83
VERTICAL	NAVD88 (feet)

SITE ANALYSIS

1. Gross tract area	31,197 SF
2. Area of dwelling	1,200 SF
3. Wooded area	NOT ESTABLISHED
4. Floodplain area	NOT ESTABLISHED
5. Net lot area	31,197 SF
6. TOTAL AREA DISTURBED	7,073 SF (AT LEAST)
7. SWM REVIEW	CONFIRM WITH CITY OF ROCKVILLE

BUILDING DATA

	G	B	FF	SF	HT	STY
111 MARYLAND AVE	—	—	—	—	20'	2

G: garage slab; B: basement; FF: finished floor; SF: subfloor; HT: height; STY: storeys. A DASH IS NOT ZERO: the elevation has not been established and must be set from a field-run topographic survey before construction.

DRAINAGE AREA COMPUTATIONS

CATCHMENT	SF	ACRES	C
Total — 4.4% Impervious	31,197	0.716	
PRE-DEVELOPMENT	SF		C
Pervious — lawn / meadow	31,197		0.25
Composite C			0.250
POST-DEVELOPMENT	SF		C
Proposed roof	1,200		0.95
Driveway and on-lot paving	177		0.95
Pervious — lawn	29,820		0.25
Composite C			0.281
Flow path	298 ft		
Flow path slope	6.0 %		
Time of concentration (Kirpich)	5.0 min		
Rainfall intensity, 10-yr	6.60 in/hr		
Peak discharge PRE, Q = CIA	1.18 cfs		
Peak discharge POST, Q = CIA	1.33 cfs		
INCREASE TO BE MANAGED	0.15 cfs		
Rv = 0.05 + 0.0091	0.0897		
Water quality volume Wqv	233 cf		

Time of concentration by Kirpich over a 298 ft flow path at 6.0%, taken from the 2 ft contours across the catchment. A 5-minute floor applies.
Rainfall intensity 6.60 in/hr for the 10-year storm at a 5.0 minute duration, NOAA Atlas 14 Vol. 2 Ver. 3, PFDS point estimate, 39.0817 N 77.1516 W.
Water quality volume on a 1.0 in rainfall, Maryland Stormwater Design Manual, Vol. 1 & 2 — WQV on a 1.0 in rainfall.
Runoff coefficients: roof and pavement 0.95, average lawn 0.25. Confirm the lawn coefficient against the soil hydrologic group before relying on the composite.
Sidewalk, curb and gutter and the driveway apron lie in the public right-of-way and drain to the street. They are excluded from the lot catchment and included in the disturbed areas.

SEQUENCE OF CONSTRUCTION

1. Pre-construction meeting
2. Obtain necessary permits
3. Notify Miss Utility at 811 at least 48 hours prior to any excavation
4. Install stabilized construction entrance and perimeter sediment control
5. Rough grade the lot
6. Construct dwelling
7. Install water, sewer and storm services and the driveway
8. Fine grade and stabilize all disturbed areas
9. Remove sediment control once the inspector gives written permission

TOTAL ESTIMATED TIME OF CONSTRUCTION: 8 MONTHS

GENERAL NOTES

1. CONTRACTOR SHALL CONTACT MISS UTILITY AT 811 A MINIMUM OF 48 HOURS PRIOR TO ANY EXCAVATION. FIELD-VERIFY LOCATION AND DEPTH BY TEST PIT BEFORE CONSTRUCTION.
2. EXISTING UTILITIES ARE SHOWN FROM PUBLIC RECORD AND ARE APPROXIMATE. LOCATION AND DEPTH SHALL BE FIELD-VERIFIED BY TEST PIT BEFORE CONSTRUCTION.
3. PROPOSED GRADE SHOWN SOLID; EXISTING GRADE SHOWN DASHED.
4. ROUGH EARTHWORK GRADES AND UTILITY ELEVATIONS SHOWN TO TENTHS OF A FOOT.
5. BOUNDARY SHOWN IS COMPILED JURISDICTION GIS, NOT A BOUNDARY SURVEY.
6. CONNECT TO EXISTING PAVEMENT, CURB AND GUTTER, DRIVEWAY AND SIDEWALK IN LINE AND GRADE.
7. NO DRIVEWAY CULVERT IS REQUIRED. THIS FRONTAGE IS AN EXISTING CURB AND GUTTER SECTION. NOT AN OPEN DITCH SECTION. GUTTER FLOW IS CARRIED THROUGH EACH ENTRANCE BY THE DEPRESSED CURB AT THE APRON PER CITY OF ROCKVILLE STANDARD. ONLY LOT DRAINAGE IS COLLECTED BY THE REAR-YARD SWALE IN THE REAR DRAINAGE EASEMENT AND CROSSES NO DRIVEWAY OR APRON.

PROFESSIONAL CERTIFICATION

I HEREBY CERTIFY THAT THESE DOCUMENTS WERE PREPARED OR APPROVED BY ME, AND THAT I AM A DULY LICENSED PROFESSIONAL ENGINEER UNDER THE LAWS OF THE STATE OF MARYLAND.

SIGNATURE DATE

SEAL LICENSE NO. EXPIRATION DATE

REVISIONS


— NONE —

SOILS TABLE USDA NRCS SSURGO

MAP UNIT	MAP UNIT NAME	K-FACT	HYDRIC	HYD. GRP	DRAINAGE CLASS
100	Dumps, refuse	—	No	—	
109D	Hyattstown channery silt loam, 15 to 25 percent slopes, very	.49	No	D	Well drained
109E	Hyattstown channery silt loam, 25 to 45 percent slopes, very	.49	No	D	Well drained
116C	Blocktown channery silt loam, 8 to 15 percent slopes, very	.49	No	D	Well drained
116D	Blocktown channery silt loam, 15 to 25 percent slopes, very	.49	No	D	Well drained
116E	Blocktown channery silt loam, 25 to 45 percent slopes, very	.49	No	D	Well drained
16B	Blocktown channery silt loams, 3 to 8 percent slopes	.43	No	C	Well drained

SOURCE AND ACCURACY
Parcel boundary — Jurisdiction gis — M-NCPPC Montgomery Planning — parcels (SDAT) — level 1
Existing contours — M-NCPPC Montgomery Planning — backgrounds/Contours_28/MapServer/1 — Contours (. . .

GRAPHIC SCALE — 1" = 30'





KEALEE

Design, build, deliver

PROJECT
111 MARYLAND AVE

ADDRESS
111 MARYLAND AVE

JURISDICTION
City of Rockville, Maryland

ZONE

SHEET
L-100 — Landscape and Tree Canopy Plan
SCALE
1" = 30'

STATUS
PRELIMINARY

SHEET NO.
5 OF 5

COORDINATES
EPSG:2248

H: NAD83

V: NAVD88 (feet)

PROFESSIONAL RESPONSIBILITY
Qualified Environmental Professional
certifies: tree_conservation

SEAL AND SIGNATURE

All content on this sheet falls within one professional scope.

PLAN TYPE AND PREPARATION

PLANT TYPE SITE DEVELOPMENT / FINE GRADING
SHEET L-100 — Landscape and Tree Canopy Plan
DISCIPLINE Landscape Architect / Qualified Professional
DRAWN BY KEALEE SITE-PLAN ENGINE
DESIGNED BY
CHECKED BY

REVISIONS

NO.	DATE	DESCRIPTION

SITE DATA

ZONE	
TAX / PARCEL ID	00150968
GROSS TRACT AREA	31,197 SF
LOT FRONTAGE	143.71'
SETBACKS	REQUIRED PROVIDED
FRONT YARD	— —
SIDE YARD	— —
REAR YARD	— —
COVERAGE	MAX PROPOSED
LOT COVERAGE	— 3.8%
BUILDING FOOTPRINT	— 1,200 SF
DATUM	
HORIZONTAL	EPSG:2248 NAD83
VERTICAL	NAVD88 (feet)

SITE ANALYSIS

1. Gross tract area	31,197 SF
2. Area of dwelling	1,200 SF
3. Wooded area	NOT ESTABLISHED
4. Floodplain area	NOT ESTABLISHED
5. Net lot area	31,197 SF
6. TOTAL AREA DISTURBED	7,073 SF (AT LEAST)
7. SWM REVIEW	CONFIRM WITH CITY OF ROCKVILLE

BUILDING DATA

	G	B	FF	SF	HT	STY
111 MARYLAND AVE	—	—	—	—	20'	2

G: garage slab; B: basement; FF: finished floor; SF: subfloor; HT: height; STY: storeys. A DASH IS NOT ZERO: the elevation has not been established and must be set from a field-run topographic survey before construction.

DRAINAGE AREA COMPUTATIONS

CATCHMENT	SF	ACRES	C
Total — 4.4% Impervious	31,197	0.716	

PRE-DEVELOPMENT	SF	C
Pervious — lawn / meadow	31,197	0.25
Composite C		0.250

POST-DEVELOPMENT	SF	C
Proposed roof	1,200	0.95
Driveway and on-lot paving	177	0.95
Pervious — lawn	29,820	0.25
Composite C		0.281

Flow path	298 ft
Flow path slope	6.0 %
Time of concentration (Kirpich)	5.0 min
Rainfall intensity, 10-yr	6.60 in/hr
Peak discharge PRE, Q = CIA	1.16 cfs
Peak discharge POST, Q = CIA	1.33 cfs
INCREASE TO BE MANAGED	0.15 cfs
Rv = 0.05 + 0.0091	0.0997
Water quality volume WQv	233 cf

Time of concentration by Kirpich over a 298 ft flow path at 6.0%, taken from the 2 ft contours across the catchment. A 5-minute floor applies.
Rainfall intensity 6.60 in/hr for the 10-year storm at a 5.0 minute duration, NOAA Atlas 14 Vol. 2 Ver. 3, PFDS point estimate, 39 0817 N 77 1516 W.
Water quality volume on a 1.0 in rainfall, Maryland Stormwater Design Manual, Vol. 1 & 2 — WQv on a 1.0 in rainfall.

Runoff coefficients: roof and pavement 0.95, average lawn 0.25. Confirm the lawn coefficient against the soil hydrologic group before relying on the composite.
Sewer, curb and gutter and the driveway apron lie in the public right-of-way and drain to the street. They are excluded from the lot catchment and included in the disturbed areas.

SEQUENCE OF CONSTRUCTION

1. Pre-construction meeting	1 DAY
2. Obtain necessary permits	2 DAYS
3. Notify Miss Utility at 811 at least 48 hours prior to any excavation	1 DAY
4. Install stabilized construction entrance and perimeter sediment control	2 DAYS
5. Rough grade the lot	5 DAYS
6. Construct dwelling	6 MONTHS
7. Install water, sewer and storm services and the driveway	10 DAYS
8. Fine grade and stabilize all disturbed areas	5 DAYS
9. Remove sediment control once the inspector gives written permission	1 DAY

TOTAL ESTIMATED TIME OF CONSTRUCTION: 8 MONTHS


GENERAL NOTES

- CONTRACTOR SHALL CONTACT MISS UTILITY AT 811 A MINIMUM OF 48 HOURS PRIOR TO ANY EXCAVATION. FIELD-VERIFY LOCATION AND DEPTH BY TEST PIT BEFORE CONSTRUCTION.
- EXISTING UTILITIES ARE SHOWN FROM PUBLIC RECORD AND ARE APPROXIMATE. LOCATION AND DEPTH SHALL BE FIELD-VERIFIED BY TEST PIT BEFORE CONSTRUCTION.
- PROPOSED GRADE SHOWN SOLID; EXISTING GRADE SHOWN DASHED.
- ROUGH EARTHWORK GRADES AND UTILITY ELEVATIONS SHOWN TO TENTHS OF A FOOT.
- BOUNDARY SHOWN IS COMPILED JURISDICTION GIS, NOT A BOUNDARY SURVEY.
- CONNECT TO EXISTING PAVEMENT, CURB AND GUTTER, DRIVEWAY AND SIDEWALK IN LINE AND GRADE.
- NO DRIVEWAY CULVERT IS REQUIRED. THIS FRONTAGE IS AN EXISTING CURB AND GUTTER SECTION. NOT AN OPEN DITCH SECTION. GUTTER FLOW IS CARRIED THROUGH EACH ENTRANCE BY THE DEPRESSED CURB AT THE APRON PER CITY OF ROCKVILLE STANDARD. ONLY LOT DRAINAGE IS COLLECTED BY THE REAR-YARD SWALE IN THE REAR DRAINAGE EASEMENT AND CROSSES NO DRIVEWAY OR APRON.

PROFESSIONAL CERTIFICATION
I HEREBY CERTIFY THAT THESE DOCUMENTS WERE PREPARED OR APPROVED BY ME, AND THAT I AM A DULY LICENSED PROFESSIONAL ENGINEER UNDER THE LAWS OF THE STATE OF MARYLAND.

SIGNATURE DATE
SEAL LICENSE NO. EXPIRATION DATE

REVISIONS
— NONE —

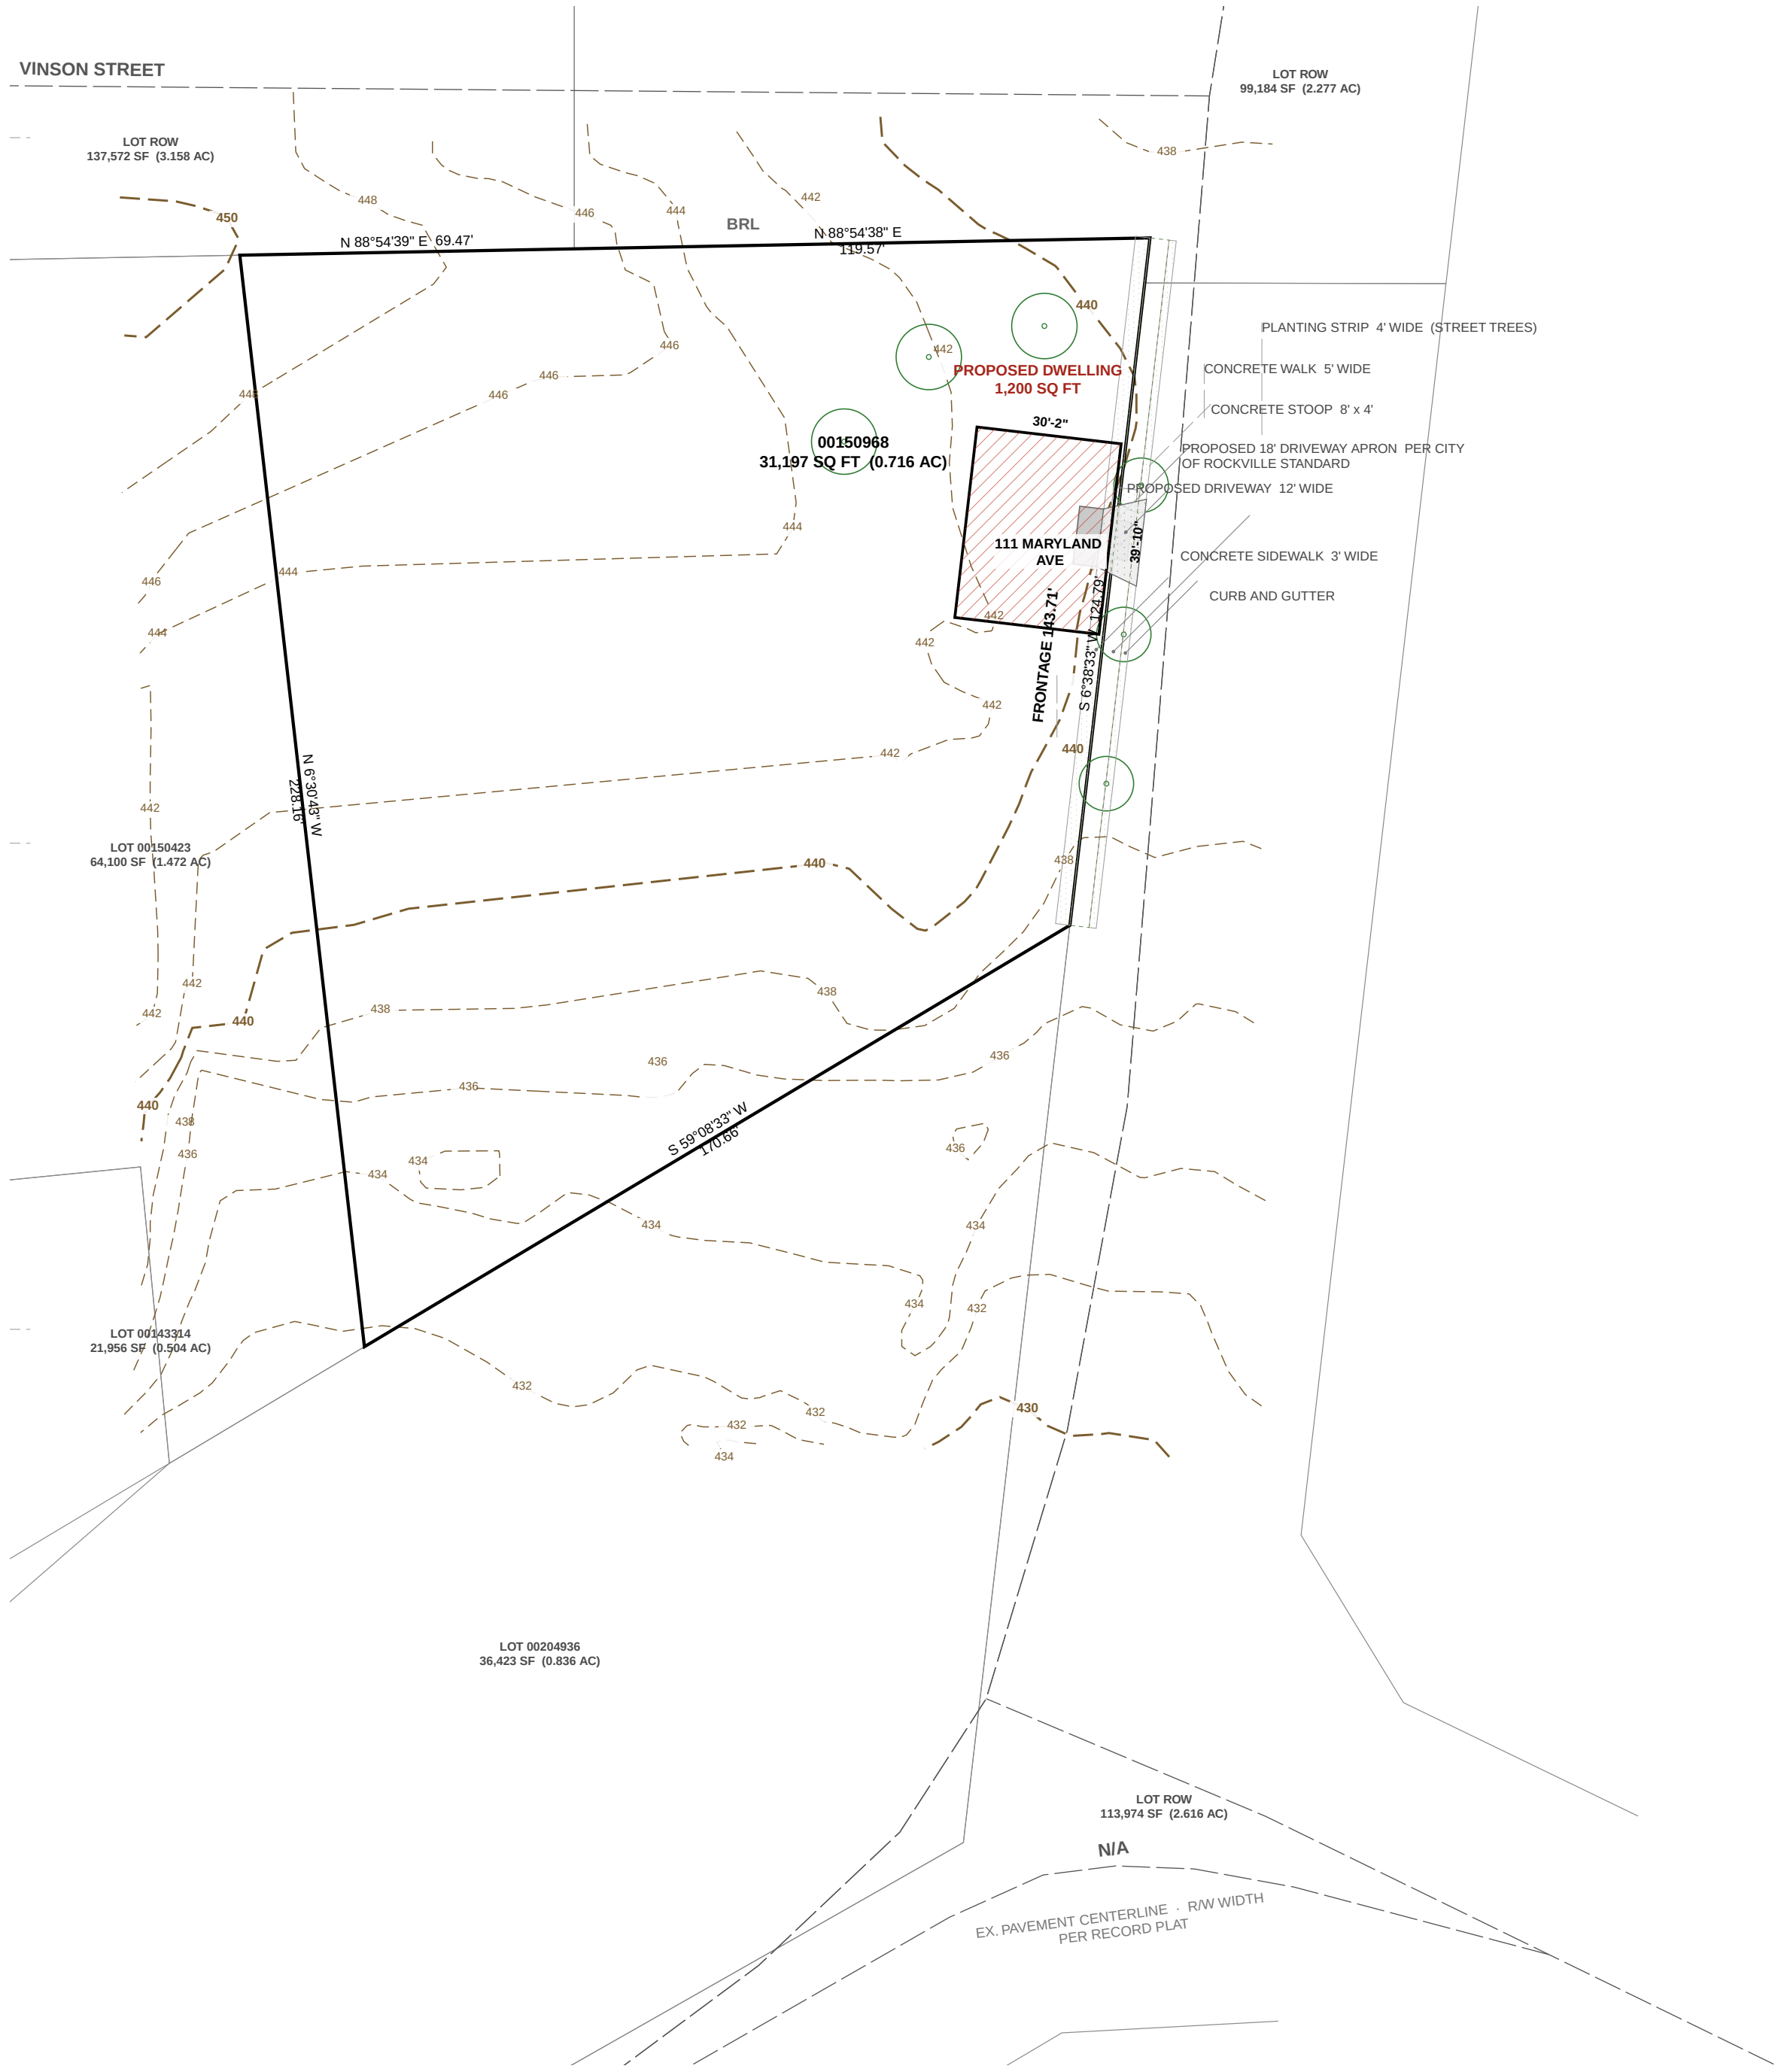

SOURCE AND ACCURACY
Parcel boundary — Jurisdiction gis — M-NCPPC Montgomery Planning — parcels (SDAT) — level 1
Existing contours — M-NCPPC Montgomery Planning — backgrounds/Contours_28/MapServer/1 — Contours (...

GRAPHIC SCALE — 1" = 30'
0 30 60 90 120 FEET
